Current Week Activities

- Level 1 – Wall/Ceiling Priming & Painting
- Level 1 – Private Dining Drywall Installation
- Level 1 – Public Bathrooms Tile Installation
- Level 2 – Roof Installation
- Level 5 – Unit Carpet Installation
- Level 9 & 10 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 10 – Residential Casework Installation
- Level 10 – Radiant Ceiling Panel Installation
- Level 11 – Unit LVT Flooring Installation
- Level 11 – Unit Bathrooms Tile Installation
- Level 12 – Wall/Ceiling Priming & Painting
- Level 14 – Insulation & Drywall Installation
- Level 15 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- East & West Site Work Progress

Upcoming Week Activities

- Level 1 – Wall/Ceiling Priming & Painting
- Level 1 – Multipurpose Room Drywall Finishing
- Level 1 – Public Bathrooms Devices & Trim
- Level 1 – Pool Scaffolding & Working Deck Removal
- Level 6 – Unit Carpet Installation
- Level 10 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 11 – Residential Casework Installation
- Level 11 – Radiant Ceiling Panel Installation
- Level 11 – Unit LVT Flooring Installation
- Level 12 – Unit Bathrooms Tile Installation
- Level 12 & 13 – Wall/Ceiling Priming & Painting
- Level 14 – Insulation & Drywall Installation
- Level 15 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- East & West Site Work Progress

Upcoming Milestone/Major Dates

- Level 15 – Enclosure
- Elevators #1 & #2 Complete

Photo #1: Southeast Structure View

Photo #2: East Site Work Progress

Photo #3: Level 1 Aerobics & Fitness Room Progress

Photo #4: Parking Level 1 Mechanical Room Equipment Progress

September 6 – September 10, 2021

Current Week Activities

- Level 1 – Wall/Ceiling Priming & Painting
- Level 1 – Pool Ceiling & Lighting Installation
- Level 1 – Public Bathrooms Tile Installation
- Level 2 – Roof Installation
- Level 4 – Unit Carpet Installation
- Level 9 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 10 – Residential Casework Installation
- Level 10 – Unit LVT Flooring Installation
- Level 11 – Unit Bathrooms Tile Installation
- Level 12 – Wall/Ceiling Priming & Painting
- Level 13 – Insulation & Drywall Installation
- Level 14 & 15 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- East & West Site Work Progress
- Tower Crane Removal

Upcoming Week Activities

- Level 1 – Wall/Ceiling Priming & Painting
- Level 1 – Multipurpose Room Drywall Finishing
- Level 1 – Public Bathrooms Tile Installation
- Level 2 – Roof Installation
- Level 5 – Unit Carpet Installation
- Level 9 & 10 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 10 – Residential Casework Installation
- Level 9 – Radiant Ceiling Panel Installation
- Level 11 – Unit LVT Flooring Installation
- Level 11 – Unit Bathrooms Tile Installation
- Level 12 – Wall/Ceiling Priming & Painting
- Level 14 – Insulation & Drywall Installation
- Level 15 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- East & West Site Work Progress

Upcoming Milestone/Major Dates

- Level 15 – Enclosure
- Elevators #1 & #2 Complete

Photo #1: Southeast Structure View & Tower Crane Removal

Photo #2: Level 4 Unit H Progress

Photo #3: Level 2 Roof Installation

Photo #4: Northwest Exterior Enclosure Progress

August 30 – September 3, 2021

Current Week Activities

- Level 1 – Wall/Ceiling Priming & Painting
- Level 5 – Unit Roller Shade Installation
- Level 8 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 8 – Radiant Ceiling Panel Installation
- Level 9 – Residential Casework Installation
- Level 9 – Unit LVT Flooring Installation
- Level 10 – Unit Bathrooms Tile Installation
- Level 11 – Wall/Ceiling Priming & Painting
- Level 12 – Insulation & Drywall Installation
- Level 13 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 14 & 15 – Interior Wall Framing
- Tower Roof Installation
- Pool Ceiling & Lighting Installation
- East Site Work Progress

Upcoming Week Activities

- Level 1 – Wall/Ceiling Priming & Painting
- Level 4 – Unit Carpet Installation
- Level 8 & 9 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 9 – Radiant Ceiling Panel Installation
- Level 9 – Residential Casework Installation
- Level 10 – Unit LVT Flooring Installation
- Level 10 – Unit Bathrooms Tile Installation
- Level 11 – Wall/Ceiling Priming & Painting
- Level 13 – Insulation & Drywall Installation
- Level 14 & 15 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 15 – Interior Wall Framing
- Tower Roof Installation
- Pool Ceiling & Lighting Installation
- East Site Work Progress

Upcoming Milestone/Major Dates

- Level 15 – Enclosure
- Tower Roof Complete

Photo #1: East Structure View

Photo #2: Level 3 Unit E Progress

Photo #3: East Site Work Progress

Photo #4: Tower Roof Installation Progress

August 16 – August 20, 2021

Current Week Activities

- Level 1 – Wall/Ceiling Priming & Painting
- Level 5 – Unit Roller Shade Installation
- Level 7 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 8 – Residential Casework Installation
- Level 8 – Radiant Ceiling Panel Installation
- Level 9 – Unit LVT Flooring Installation
- Level 9 – Unit Bathrooms Tile Installation
- Level 10 – Wall/Ceiling Priming & Painting
- Level 12 – Insulation & Drywall Installation
- Level 13 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 14 & 15 – Interior Wall Framing
- Level 15 – Window Wall Installation
- Tower Roof Installation
- East Site Work Progress

Upcoming Week Activities

- Level 1 – Wall/Ceiling Priming & Painting
- Level 4 – Unit Carpet Installation
- Level 7 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 8 – Radiant Ceiling Panel Installation
- Level 9 – Residential Casework Installation
- Level 9 – Unit LVT Flooring Installation
- Level 10 – Unit Bathrooms Tile Installation
- Level 11 – Wall/Ceiling Priming & Painting
- Level 12 – Insulation & Drywall Installation
- Level 14 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 14 & 15 – Interior Wall Framing
- Level 15 – Window Wall Installation
- Tower Roof Installation
- East Site Work Progress

Upcoming Milestone/Major Dates

- Level 15 – Enclosure
- Tower Roof Complete

Photo #1: East Structure View

Photo #2: Zingsheim Room In-Wall Rough-In

Photo #3: Elevator #1 Entrance Door Installation

Photo #4: Level 3 Unit L Appliance Mockup

August 9 – August 13, 2021

Current Week Activities

- Level 2 – Units Punch List Review
- Level 4 – Unit Carpet Installation
- Level 7 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 7 – Radiant Ceiling Panel Installation
- Level 8 – Residential Casework Installation
- Level 8 – Unit LVT Flooring Installation
- Level 9 – Unit Bathrooms Tile Installation
- Level 10 – Wall/Ceiling Priming & Painting
- Level 10 & 11 – Exterior Metal Panel Installation
- Level 11 – Insulation & Drywall Installation
- Level 13 & 14 – Interior Wall Framing
- Level 15 – Window Wall Installation
- Tower Roof Installation
- Northeast Site Work Progress

Upcoming Week Activities

- Level 4 – Unit Carpet Installation
- Level 7 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 8 – Residential Casework Installation
- Level 8 – Radiant Ceiling Panel Installation
- Level 9 – Unit LVT Flooring Installation
- Level 9 – Unit Bathrooms Tile Installation
- Level 10 – Wall/Ceiling Priming & Painting
- Level 10 & 11 – Exterior Metal Panel Installation
- Level 12 – Insulation & Drywall Installation
- Level 13 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 14 & 15 – Interior Wall Framing
- Level 15 – Window Wall Installation
- Tower Roof Installation
- East Site Work Progress

Upcoming Milestone/Major Dates

- Level 15 – Enclosure
- Tower Roof Complete

Photo #1: East Structure View

Photo #2: Level 1 Fireplace Rough-In

Photo #3: Northeast Site Work Progress

Photo #4: Level 3 Unit B Progress

August 2 – August 6, 2021

Current Week Activities

- Level 2 – Units Construction Clean
- Level 6 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 6 – Residential Casework Countertop Installation
- Level 7 – Radiant Ceiling Panel Installation
- Level 7 – Residential Casework Installation
- Level 7 – Unit LVT Flooring Installation
- Level 8 – Unit Bathrooms Tile Installation
- Level 9 – Wall/Ceiling Priming & Painting
- Level 10 – Exterior Metal Panel Installation
- Level 10 – Insulation & Drywall Installation
- Level 12 & 13 – Interior Wall Framing
- Level 15 – Window Wall Installation
- Tower Roof Installation
- Northeast Site Work Progress

Upcoming Week Activities

- Level 4 – Unit Carpet Installation
- Level 6 & 7 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 7 – Residential Casework Countertop Installation
- Level 7 & 8 – Radiant Ceiling Panel Installation
- Level 7 – Residential Casework Installation
- Level 7 – Unit LVT Flooring Installation
- Level 8 – Unit Bathrooms Tile Installation
- Level 9 – Wall/Ceiling Priming & Painting
- Level 10 & 11 – Exterior Metal Panel Installation
- Level 11 – Insulation & Drywall Installation
- Level 13 & 14 – Interior Wall Framing
- Level 15 – Window Wall Installation
- Tower Roof Installation
- Northeast Site Work Progress

Upcoming Milestone/Major Dates

- Level 15 – Enclosure
- Tower Roof Complete

Photo #1: Southeast Structure View

Photo #2: Northeast Site Work Progress

Photo #3: Northwest Exterior Enclosure Progress

Photo #4: Level 6 Unit I Progress

July 19 – July 23, 2021

Current Week Activities

- Level 2 – Units Construction Clean
- Level 5 & 6 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 6 – Residential Casework Countertop Installation
- Level 6 & 7 – Radiant Ceiling Panel Installation
- Level 7 – Residential Casework Installation
- Level 7 – Unit LVT Flooring Installation
- Level 7 – Unit Bathrooms Tile Installation
- Level 8 – Wall/Ceiling Priming & Painting
- Level 9 & 10 – Exterior Metal Panel Installation
- Level 10 – Insulation & Drywall Installation
- Level 11 – Interior Wall Framing
- Level 14 & 15 – Window Wall Installation
- Tower Roof Installation
- Northeast Site Work Progress

Upcoming Week Activities

- Level 2 – Units Construction Clean
- Level 6 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 6 – Residential Casework Countertop Installation
- Level 7 – Radiant Ceiling Panel Installation
- Level 7 – Residential Casework Installation
- Level 7 – Unit LVT Flooring Installation
- Level 8 – Unit Bathrooms Tile Installation
- Level 9 – Wall/Ceiling Priming & Painting
- Level 10 – Exterior Metal Panel Installation
- Level 10 – Insulation & Drywall Installation
- Level 12 & 13 – Interior Wall Framing
- Level 15 – Window Wall Installation
- Tower Roof Installation
- Northeast Site Work Progress

Upcoming Milestone/Major Dates

- Level 15 – Enclosure
- Tower Roof Complete

Photo #1: Southeast Structure View

Photo #2: Northwest Enclosure Progress

Photo #3: Level 3 Unit E Progress

Photo #4: Level 5 Unit L Progress

July 12 – July 16, 2021

Photo #1: Northeast Structure View

Current Week Activities

- Level 1 – Drywall Installation
- Level 3 – Window Shades Installation
- Level 4 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 5 – Residential Casework Countertop Installation
- Level 5 & 6 – Radiant Ceiling Panel Installation
- Level 6 – Residential Casework Installation
- Level 6 – Unit LVT Flooring Installation
- Level 6 & 7 – Unit Bathrooms Tile Installation
- Level 7 – Wall/Ceiling Priming & Painting
- Level 8 & 9 – Exterior Metal Panel Installation
- Level 9 – Insulation & Drywall Installation
- Level 10 & 11 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 11 – Interior Wall Framing
- Level 13 & 14 – Window Wall Installation

Photo #2: Level 2 Unit D Progress

Upcoming Week Activities

- Level 1 – Drywall Installation
- Level 4 – Window Shades Installation
- Level 5 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 5 – Residential Casework Countertop Installation
- Level 6 – Radiant Ceiling Panel Installation
- Level 6 – Residential Casework Installation
- Level 7 – Unit LVT Flooring Installation
- Level 7 – Unit Bathrooms Tile Installation
- Level 8 – Wall/Ceiling Priming & Painting
- Level 8 & 9 – Exterior Metal Panel Installation
- Level 9 – Insulation & Drywall Installation
- Level 11 – Interior Wall Framing
- Level 11 & 12 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 14 & 15 – Window Wall Installation

Photo #3: Unit Roller Shade Installation

Upcoming Milestone/Major Dates

- Level 14 – Enclosure
- Level 15 – Enclosure

Photo #4: Level 9 Drywall Installation & Concrete Ceiling Preparation

June 28 – July 2, 2021

Photo #1: Northwest Structure View

Current Week Activities

- Topping Out Celebration – June 24th
- Level 1 – Drywall Installation
- Level 2 – Window Shades Installation
- Level 3 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 4 – Residential Casework Countertop Installation
- Level 4 & 5 – Radiant Ceiling Panel Installation
- Level 5 – Residential Casework Installation
- Level 5 & 6 – Unit Bathrooms Tile Installation
- Level 6 – Unit LVT Flooring Installation
- Level 7 – Wall/Ceiling Priming & Painting
- Level 8 – Insulation & Drywall Installation
- Level 9 & 10 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 11 – Interior Wall Framing
- Level 12 & 13 – Window Wall Installation

Photo #2: Generator Placement

Upcoming Week Activities

- Level 1 – Drywall Installation
- Level 3 – Window Shades Installation
- Level 4 – Mechanical, Electrical & Plumbing Devices & Trim
- Level 5 – Residential Casework Countertop Installation
- Level 5 & 6 – Radiant Ceiling Panel Installation
- Level 6 – Residential Casework Installation
- Level 6 – Unit LVT Flooring Installation
- Level 6 & 7 – Unit Bathrooms Tile Installation
- Level 7 – Wall/Ceiling Priming & Painting
- Level 8 & 9 – Exterior Metal Panel Installation
- Level 9 – Insulation & Drywall Installation
- Level 10 & 11 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 11 – Interior Wall Framing
- Level 13 & 14 – Window Wall Installation

Photo #3: Level 2 Unit F Kitchen

Upcoming Milestone/Major Dates

- Level 13 – Enclosure
- Level 14 – Enclosure

Photo #4: Level 1 East Corridor Progress

June 21 – June 25, 2021

Photo #1: Southeast Structure View

Current Week Activities

- Level 16 – Eyebrow Pours
- Level 1 – Drywall Installation
- Level 7 & 8 – Exterior Metal Panel Installation
- Level 3 – Radiant Ceiling Panel Installation
- Level 3 – Residential Casework Countertop Installation
- Level 5 – Residential Casework Installation
- Level 5 – Unit LVT Flooring Installation
- Level 5 – Unit Bathrooms Tile Installation
- Level 6 – Wall/Ceiling Priming & Painting
- Level 8 – Insulation & Drywall Installation
- Level 9 & 10 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 10 – Interior Wall Framing
- Level 12 – Window Wall Installation

Photo #2: Level 1 East Enclosure Progress

Upcoming Week Activities

- Level 1 – Drywall Installation
- Level 2 – Window Shades Installation
- Level 3 – Mechanical, Electrical & Plumbing Accessories Installation
- Level 4 – Residential Casework Countertop Installation
- Level 4 & 5 – Radiant Ceiling Panel Installation
- Level 5 – Residential Casework Installation
- Level 5 & 6 – Unit Bathrooms Tile Installation
- Level 6 – Unit LVT Flooring Installation
- Level 7 – Wall/Ceiling Priming & Painting
- Level 8 – Insulation & Drywall Installation
- Level 8 – Exterior Metal Panel Installation
- Level 9 & 10 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 11 – Interior Wall Framing
- Level 12 & 13 – Window Wall Installation
- Level 16 – Elevator Hoisting Framing Installation

Photo #3: Level 1 Chapel Ceiling Progress

Upcoming Milestone/Major Dates

- Level 13 – Enclosure
- Topping Out Celebration – June 24th

Photo #4: Level 4 Corridor Progress

June 14 – June 18, 2021

Photo #1: Southeast Structure View

Current Week Activities

- Level 16 – Eyebrow Pours
- Level 1 – Drywall Installation
- Level 6 & 7 – Exterior Metal Panel Installation
- Level 2 – Mechanical, Electrical & Plumbing Accessories Installation
- Level 2 – Residential Casework Countertop Installation
- Level 3 – Radiant Ceiling Panel Installation
- Level 4 – Residential Casework Installation
- Level 5 – Unit LVT Flooring Installation
- Level 5 – Unit Bathrooms Tile Installation
- Level 6 – Wall/Ceiling Priming & Painting
- Level 7 – Insulation & Drywall Installation
- Level 9 & 10 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 10 – Wall Framing
- Level 11 & 12 – Window Wall Installation

Photo #2: Level 2 Benchmark Unit I - Contemporary

Photo #3: Level 2 Benchmark Unit K - Traditional

Photo #4: Level 2 Benchmark Unit L - Modern

Upcoming Week Activities

- Level 16 – Eyebrow Pours
- Level 1 – Drywall Installation
- Level 7 & 8 – Exterior Metal Panel Installation
- Level 2 – Mechanical, Electrical & Plumbing Accessories Installation
- Level 3 – Radiant Ceiling Panel Installation
- Level 3 – Residential Casework Countertop Installation
- Level 5 – Residential Casework Installation
- Level 5 – Unit LVT Flooring Installation
- Level 5 – Unit Bathrooms Tile Installation
- Level 6 – Wall/Ceiling Priming & Painting
- Level 8 – Insulation & Drywall Installation
- Level 9 & 10 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 10 – Wall Framing
- Level 12 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 12 – Enclosure
- Level 16 – Structure

June 7 – June 11, 2021

Current Week Activities

- Level 16 – Eyebrow Pours
- Roof – Post-Tension Deck Concrete Pours #3
- Level 1 – Drywall Installation
- Level 5, 6, 7 & 8 – Exterior Metal Panel Installation
- Level 2 – Countertop Installation
- Level 2 – Radiant Ceiling Panel Installation
- Level 4 – Residential Casework Installation
- Level 5 – Unit LVT Flooring Installation
- Level 6 – Wall/Ceiling Priming & Painting
- Level 5 – Unit Bathrooms Tile Installation
- Level 7 – Insulation & Drywall Installation
- Level 9 & 10 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 9 – Wall Framing
- Level 11 & 12 – Window Wall Installation

Upcoming Week Activities

- Level 16 – Eyebrow Pours
- Level 1 – Drywall Installation
- Level 6, 7 & 8 – Exterior Metal Panel Installation
- Level 4 – Residential Casework Countertop Installation
- Level 2 – Mechanical, Electrical & Plumbing Accessories Installation
- Level 3 – Radiant Ceiling Panel Installation
- Level 5 – Residential Casework Installation
- Level 5 – Unit LVT Flooring Installation
- Level 5 – Unit Bathrooms Tile Installation
- Level 6 – Wall/Ceiling Priming & Painting
- Level 7 – Insulation & Drywall Installation
- Level 9 & 10 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 10 – Wall Framing
- Level 11 & 12 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 11– Enclosure
- Level 16 – Structure

Photo #1: Roof Deck Pour #3 Shoring

Photo #2: Level 16 Pour #1

Photo #3: Level 3 Unit L Residential Casework Installation

Photo #4: West Exterior Window Wall & Metal Panel Progress

May 31 – June 5, 2021

Current Week Activities

- Level 15 – Concrete Balcony Pours
- Roof – Post-Tension Deck Concrete Pours #1 & #2
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1, 4, 5, & 6 – Exterior Metal Panel Installation
- Level 2 – Acoustical Ceiling Installation
- Level 2 & 3 – Radiant Ceiling Panel Installation
- Level 3 – Residential Casework Installation
- Level 3 – Unit LVT Flooring Installation
- Level 5 – Wall/Ceiling Priming & Painting
- Level 4 – Unit Bathrooms Tile Installation
- Level 6 – Insulation & Drywall Installation
- Level 8 & 9 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 9 – Wall Framing
- Level 10 & 11 – Window Wall Installation

Upcoming Week Activities

- Roof – Post-Tension Deck Concrete Pours #3
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1, 5, & 6 – Exterior Metal Panel Installation
- Level 2 – Residential Casework Countertop Installation
- Level 2 – Mechanical, Electrical & Plumbing Accessories Installation
- Level 2 & 3 – Radiant Ceiling Panel Installation
- Level 4 – Residential Casework Installation
- Level 4 – Unit LVT Flooring Installation
- Level 4 – Unit Bathrooms Tile Installation
- Level 5 – Wall/Ceiling Priming & Painting
- Level 7 – Insulation & Drywall Installation
- Level 8 & 9 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 9 – Wall Framing
- Level 11 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 11– Enclosure
- Level 15 – Structure

Photo #1: Roof Deck Pour #2 Pre-Pour

Photo #2: Level 2 Corridor Progress

Photo #3: Level 2 Unit L Residential Casework Installation

Photo #4: East Exterior Stone Progress

May 24 – May 28, 2021

Photo #1: Southeast Structure View

Current Week Activities

- Level 14 & 15 – Concrete Balcony Pours
- Level 15 – Post-Tension Deck Concrete Pour #3
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1, 2, 3, 4, 5, & 6 – Exterior Metal Panel Installation
- Level 2 – Radiant Ceiling Panel Installation
- Level 2 & 3 – Residential Casework Installation
- Level 3 – Unit LVT Flooring Installation
- Level 4 – Wall/Ceiling Priming & Painting
- Level 4 – Unit Bathrooms Tile Installation
- Level 6 – Insulation & Drywall Installation
- Level 7 & 8 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 9 – Priority Wall Framing
- Level 10 – Window Wall Installation

Photo #2: Level 1 Chapel Progress

Upcoming Week Activities

- Level 15 – Concrete Balcony Pours
- Roof – Post-Tension Deck Concrete Pours #1 & #2
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1, 4, 5, & 6 – Exterior Metal Panel Installation
- Level 2 – Acoustical Ceiling Installation
- Level 2 – Radiant Ceiling Panel Installation
- Level 3 – Residential Casework Installation
- Level 3 – Unit LVT Flooring Installation
- Level 5 – Wall/Ceiling Priming & Painting
- Level 4 – Unit Bathrooms Tile Installation
- Level 6 – Insulation & Drywall Installation
- Level 8 & 9 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 9 – Wall Framing
- Level 10 & 11 – Window Wall Installation

Photo #3: Level 1 Aerobics Room Above-Ceiling Progress

Upcoming Milestone/Major Dates

- Level 10 – Enclosure
- Level 15 – Structure

Photo #4: Level 2 Unit A Residential Casework Installation

May 17 – May 21, 2021

Current Week Activities

- Level 14 – Concrete Balcony Pours
- Level 15 – Post-Tension Deck Concrete Pours #1 & #2
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1, 2, 3, 4, 5, & 6 – Exterior Metal Panel Installation
- Level 3 – Unit Bathrooms Tile Installation
- Level 3 – Unit LVT Flooring Installation
- Level 2 – Residential Casework Installation
- Level 4 – Wall/Ceiling Priming & Painting
- Level 5 – Insulation & Drywall Installation
- Level 7 & 8 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 8 – Priority Wall Framing
- Level 9 & 10 – Window Wall Installation

Upcoming Week Activities

- Level 14 & 15 – Concrete Balcony Pours
- Level 15 – Post-Tension Deck Concrete Pour #3
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1, 2, 3, 4, 5, & 6 – Exterior Metal Panel Installation
- Level 2 – Radiant Ceiling Panel Installation
- Level 2 & 3 – Residential Casework Installation
- Level 3 – Unit LVT Flooring Installation
- Level 4 – Wall/Ceiling Priming & Painting
- Level 4 – Unit Bathrooms Tile Installation
- Level 6 – Insulation & Drywall Installation
- Level 7 & 8 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 9 – Priority Wall Framing
- Level 10 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 9 – Enclosure
- Level 14 – Structure

Photo #1: Southeast Structure View

Photo #2: Level 15 Active Deck View

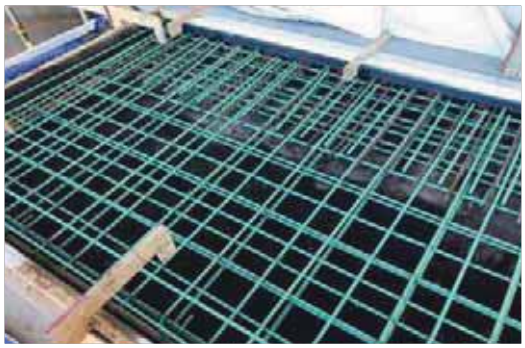

Photo #3: Level 14 Unit I Balcony Reinforcement

Photo #4: Level 2 Unit D Flooring Installation

May 10 – May 14, 2021

Current Week Activities

- Level 12 & 13 – Concrete Balcony Pours
- Level 14 – Post-Tension Deck Concrete Pour #3
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1, 2, 3, 4, 5, & 6 – Exterior Metal Panel Installation
- Level 2 – Unit Bathrooms Tile Installation
- Level 2 – Unit RFT Flooring Installation
- Level 2 – Residential Casework Installation
- Level 3 – Wall/Ceiling Priming & Painting
- Level 5 – Insulation & Drywall Installation
- Level 6 & 7 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 8 – Priority Wall Framing
- Level 8 & 9 – Window Wall Installation

Upcoming Week Activities

- Level 14 – Concrete Balcony Pours
- Level 15 – Post-Tension Deck Concrete Pours #1 & #2
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1, 2, 3, 4, 5, & 6 – Exterior Metal Panel Installation
- Level 3 – Unit Bathrooms Tile Installation
- Level 3 – Unit RFT Flooring Installation
- Level 2 – Residential Casework Installation
- Level 4 – Wall/Ceiling Priming & Painting
- Level 5 – Insulation & Drywall Installation
- Level 7 & 8 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 8 – Priority Wall Framing
- Level 9 & 10 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 9 – Enclosure
- Level 14 – Structure

Photo #1: Southeast Structure View

Photo #2: Level 14 Post-Tension Deck Pour #3 Pre-Pour

Photo #3: Level 2 Unit G Shower Tile Installation

Photo #4: Level 2 Unit I Residential Casework Installation

May 3 – May 7, 2021

Current Week Activities

- Level 12 – Concrete Balcony Pours
- Level 13 – Post-Tension Deck Concrete Pour #2 & #3
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Dining Room Ceiling Rough-In
- Levels 1 - 5 – Exterior Metal Panel Installation
- Level 2 – Wall/Ceiling Priming & Painting
- Level 2 – Unit I Shower Mockup
- Level 2 – Tile Installation
- Level 4 – Insulation & Drywall Installation
- Level 5 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 6 – Wall Framing
- Level 7 & 8 – Window Wall Installation

Upcoming Week Activities

- Elevator Core #2 – Form System Breakdown
- Level 12 & 13 – Concrete Balcony Pours
- Level 14 – Post-Tension Deck Concrete Pour #1
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Dining Room Ceiling Rough-In
- Levels 1, 2, 3, & 4 – Exterior Metal Panel Installation
- Levels 2 & 3 – Wall/Ceiling Priming & Painting
- Level 4 – Insulation & Drywall Installation
- Levels 5 & 6 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 6 – Wall Framing
- Level 7 – Priority Wall Framing
- Level 8 & 9 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 8 – Enclosure
- Level 12 – Structure

Photo #1: Northeast Structure View

Photo #2: Pool Progress

Photo #3: Level 1 Interior Rough-In and Framing Progress

Photo #4: Level 13 Post-Tension Deck Pour #3 Pre-Pour

April 19 – April 23, 2021

Current Week Activities

- Elevator Core 1 – Level 17 Concrete Pour. Last Lift!!
- Level 11 – Concrete Balcony Pours
- Level 12 – Post-Tension Deck Concrete Pour #3
- Level 13 – Post-Tension Deck Concrete Pour #1
- Parking Level 1 – West Exterior Stone Installation
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Whirlpool Wall Installation
- Levels 1, 2, 3, & 4 – Exterior Metal Panel Installation
- Level 2 – Wall/Ceiling Priming & Painting
- Level 3 – Insulation & Drywall Installation
- Level 4 & 5 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 6 – Priority Wall Framing
- Level 7 & 8 – Window Wall Installation

Upcoming Week Activities

- Level 12 – Concrete Balcony Pours
- Level 13 – Post-Tension Deck Concrete Pour #2
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Dining Room Ceiling Rough-In
- Levels 1, 2, 3, & 4 – Exterior Metal Panel Installation
- Level 2 – Wall/Ceiling Priming & Painting
- Level 2 – Unit I Tile Shower Benchmark
- Level 4 – Insulation & Drywall Installation
- Level 5 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 6 – Wall Framing
- Level 7 & 8 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 7 – Enclosure
- Level 12 – Structure

Photo #1: Southeast Structure View

Photo #2: Corridor Prior to Drywall

Photo #3: Level 2 Corridor Post Drywall and Primed

Photo #4: Level 13 Post-Tension Deck Pour #1 Pre-Pour

April 12 – April 16, 2021

Current Week Activities

- Elevator Core 2 – Level 14 Concrete Pour
- Level 11 – Concrete Balcony Pours
- Level 12 – Post-Tension Deck Concrete Pour #2
- Parking Level 1 – West Exterior Stone Installation
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Soffit Framing
- Level 1 – Pool Wall Installation
- Levels 1, 2, & 3 – Exterior Metal Panel Installation
- Level 3 – Insulation & Drywall Installation
- Level 4 & 5 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 6 & 7 – Window Wall Installation

Upcoming Week Activities

- Elevator Core 1 – Level 17 Concrete Pour. Last Lift!!
- Level 11 – Concrete Balcony Pours
- Level 12 – Post-Tension Deck Concrete Pour #3
- Parking Level 1 – West Exterior Stone Installation
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Dining Room Ceiling Rough-In
- Level 1 – Whirlpool Wall Installation
- Levels 1, 2, 3, & 4 – Exterior Metal Panel Installation
- Level 3 – Insulation & Drywall Installation
- Level 4 & 5 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 6 – Priority Wall Framing
- Level 7 & 8 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 7 – Enclosure
- Level 11 – Structure

Photo #1: Southeast Structure View

Photo #2: West Parking Level 1 Exterior Stone

Photo #3: Level 2 Interior Progress

Photo #4: Level 12 Window-Washing Davit Reinforcement

April 5 – April 9, 2021

Current Week Activities

- Elevator Core 1 – Level 15 to Roof Concrete Pour
- Level 10 – Concrete Balcony Pours
- Level 12 – Post-Tension Deck Concrete Pour #1
- Parking Level 1 – West Exterior Stone Installation
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Soffit Framing
- Level 1 – Pool Floor Concrete Pour
- Levels 1, 2, & 3 – Exterior Metal Panel Installation
- Level 2 – Insulation & Drywall Installation
- Level 4 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 6 – Window Wall Installation
- Level 7 – Exterior Pre-fabricated Wall Panel Installation

Upcoming Week Activities

- Elevator Core 2 – Level 14 Concrete Pour
- Level 11 – Concrete Balcony Pours
- Level 12 – Post-Tension Deck Concrete Pour #2
- Parking Level 1 – West Exterior Stone Installation
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Soffit Framing
- Level 1 – Pool Wall Installation
- Levels 1, 2, & 3 – Exterior Metal Panel Installation
- Level 3 – Insulation & Drywall Installation
- Level 4 & 5 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 6 & 7 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 6 – Enclosure
- Level 11 – Structure

Photo #1: Northwest Structure View

Photo #2: Pool Installation Pre-Pour

Photo #3: Parking Level 1 Exterior Stone Installation

Photo #4: Parking Level 1 Fire Pump Piping

March 29 – April 2, 2021

Current Week Activities

- Elevator Core 1 – Level 15 Concrete Pour
- Level 10 – Concrete Balcony Pours
- Level 11 – Post-Tension Deck Concrete Pour #2
- Level 12 – Post-Tension Deck Framing
- Parking Level 1 – Mechanical Room Rough-In
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Soffit Framing
- Levels 1 & 2 – Exterior Metal Panel Installation
- Level 2 – Insulation & Drywall Installation
- Level 3 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 5 – Window Wall Installation
- Level 6 – Exterior Pre-fabricated Wall Panel Installation

Upcoming Week Activities

- Elevator Core 2 – Level 14 Concrete Pour
- Level 10 – Concrete Balcony Pours
- Level 11 – Post-Tension Deck Concrete Pour #3
- Parking Level 1 – Exterior Stone Installation
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Soffit Framing
- Level 1 – Pool Installation Rough-In
- Levels 1, 2, & 3 – Exterior Metal Panel Installation
- Level 2 – Insulation & Drywall Installation
- Level 4 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 6 – Window Wall Installation
- Level 7 – Exterior Pre-fabricated Wall Panel Installation

Upcoming Milestone/Major Dates

- Level 5 – Enclosure
- Level 10 – Structure

Photo #1: Northwest Structure View

Photo #2: Level 10 Unit L Balcony

Photo #3: Level 11 Post-Tension Deck Pour #3 Pre-Pour

Photo #4: Level 1 Pool Piping

March 22 – March 26, 2021

Current Week Activities

- Elevator Core 1 – Level 14 Concrete Pour
- Elevator Core 2 – Level 13 Concrete Pour
- Level 9 – Concrete Balcony Pours
- Level 10 – Post-Tension Deck Concrete Pour #3
- Level 11 – Post-Tension Deck Concrete Pour #1
- Parking Level 1 – Mechanical Room Rough-In
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Wall Framing
- Levels 1 & 2 – Exterior Metal Panel Installation
- Level 2 – Interior Wall Rough-In Inspections
- Level 3 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 5 – Window Wall Installation

Upcoming Week Activities

- Elevator Core 1 – Level 15 Concrete Pour
- Level 10 – Concrete Balcony Pours
- Level 11 – Post-Tension Deck Concrete Pour #2
- Parking Level 1 – Mechanical Room Rough-In
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Soffit Framing
- Levels 1 & 2 – Exterior Metal Panel Installation
- Level 2 – Insulation & Drywall Installation
- Level 3 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 5 – Window Wall Installation
- Level 6 – Exterior Pre-fabricated Wall Panel Installation

Upcoming Milestone/Major Dates

- Level 5 – Enclosure
- Level 10 – Structure

Photo #1: East Structure View

Photo #2: Level 10 Unit D East View

Photo #3: Levels 2-5 Exterior Enclosure Progress

Photo #4: Level 1 Locker Room CMU Installation

March 15 – March 19, 2021

Current Week Activities

- Elevator Core 2 – Level 12 Concrete Pour
- Level 9 – Concrete Balcony Pours
- Level 10 – Post-Tension Deck Concrete Pour #2
- Level 11 – Post-Tension Deck Framing
- Parking Level 1 – Mechanical Room Rough-In
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Priority Wall Framing
- Level 2 – Exterior Metal Panel Installation
- Level 2 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 3 – Interior Wall Framing
- Level 4 – Window Wall Installation
- Site – Chiller Pad Piping

Upcoming Week Activities

- Elevator Core 1 – Level 14 Concrete Pour
- Level 9 – Concrete Balcony Pours
- Level 10 – Post-Tension Deck Concrete Pour #3
- Level 11 – Post-Tension Deck Concrete Pour #1
- Parking Level 1 – Mechanical Room Rough-In
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Priority Wall Framing
- Levels 1 & 2 – Exterior Metal Panel Installation
- Level 2 – Interior Wall Rough-In Inspections
- Level 3 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 5 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 4 – Enclosure
- Level 9 – Structure
- Level 1 – Enclosure

Photo #1: East Structure View

Photo #2: Level 9 Unit L South View

Photo #3: Level 10 Post-Tension Deck Pre-Pour

Photo #4: Levels 2-4 Exterior Enclosure Progress

March 8 – March 12, 2021

Current Week Activities

- Elevator Core 1 – Level 13 Concrete Pour
- Level 8 & 9 – Concrete Balcony Pours
- Level 9 – Post-Tension Deck Concrete Pour # 3
- Level 10 – Post-Tension Deck Concrete Pour #1
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Priority Wall Framing
- Level 2 – Exterior Metal Panel Benchmark Installation
- Level 2 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 3 – Interior Priority Wall Framing
- Level 4 – Window Wall Installation
- Level 5 – Exterior Prefabricated Wall Panel Installation

Upcoming Week Activities

- Elevator Core 2 – Level 12 Concrete Pour
- Level 9 – Concrete Balcony Pours
- Level 10 – Post-Tension Deck Concrete Pour #2
- Level 11 – Post-Tension Deck Framing
- Parking Level 1 – Mechanical Room Rough-In
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Priority Wall Framing
- Level 2 – Exterior Metal Panel Installation
- Level 2 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 3 – Interior Wall Framing
- Level 4 – Window Wall Installation
- Site – Chiller Pad Piping

Upcoming Milestone/Major Dates

- Level 4 – Enclosure
- Level 9 – Structure
- Level 1 – Enclosure

Photo #1: East Structure View

Photo #2: Elevator Core #2 View

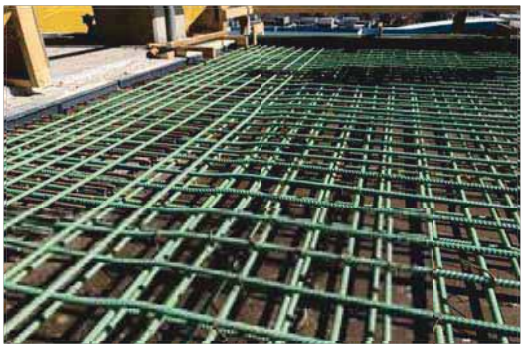

Photo #3: Level 8 Balcony Reinforcement

Photo #4: Level 1 Interior Progress

March 1 – March 5, 2021

Current Week Activities

- Elevator Core 1 – Level 12 Concrete Pour
- Elevator Core 2 – Level 11 Concrete Pour
- Level 8 – Concrete Balcony Pours
- Level 9 – Post-Tension Deck Pour # 1 & # 2
- Parking Level 1 – Mechanical, Electrical & Plumbing Rough-In
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Priority Wall Framing
- Level 2 – Interior Wall Framing
- Level 2 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 3 – Interior Priority Wall Framing
- Level 3 – Window Wall Installation

Upcoming Week Activities

- Elevator Core 1 – Level 13 Concrete Pour
- Level 8 – Concrete Balcony Pours
- Level 9 – Post-Tension Deck Pour # 3
- Level 10 – Post-Tension Deck Framing & Reinforcement
- Parking Level 1 – Mechanical Room Rough-In
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Priority Wall Framing
- Level 2 – Exterior Metal Panel Benchmark Installation
- Level 2 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 3 – Interior Priority Wall Framing
- Level 4 – Window Wall Installation
- Level 5 – Exterior Prefabricated Wall Panel Installation

Upcoming Milestone/Major Dates

- Level 4 – Enclosure
- Level 8 – Structure
- Level 1 – Enclosure

Photo #1: Southeast Structure View

Photo #2: Level 9 Post-Tension Pour #2 Pre-Pour

Photo #3: Northwest Corner Exterior Enclosure Progress

Photo #4: Level 8 Balcony Reinforcement

Current Week Activities

- Levels 7 & 8 – Concrete Balcony Pours
- Level 8 – Post-Tension Concrete Deck Pour #3
- Level 9 – Post-Tension Deck Framing
- Parking Level 1 – Mechanical, Electrical & Plumbing Overhead
- Parking Level 1 – Air Handling Unit Delivery & Installation
- Level 1 – Interior Priority Wall Framing
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 2 – Interior Wall Framing
- Level 2 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 3 – Window Wall Installation
- Level 4 – Exterior Framing and Sheathing Panel Installation
- Site – Winter Weather Conditions

Upcoming Week Activities

- Elevator Core 1 – Level 13 Concrete Pour
- Level 8 – Concrete Balcony Pours
- Level 9 – Post-Tension Deck Framing & Reinforcement
- Level 9 – Post-Tension Deck Pour # 1
- Parking Level 1 – Mechanical, Electrical & Plumbing Rough-In
- Level 1 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Interior Priority Wall Framing
- Level 2 – Interior Wall Framing
- Level 2 – Mechanical, Electrical, Plumbing & Fire Protection Rough-In
- Level 3 – Interior Priority Wall Framing
- Level 3 – Window Wall Installation

Upcoming Milestone/Major Dates

- Level 4 – Enclosure
- Level 8 – Structure
- Level 1 – Enclosure

Photo #1: Southeast Structure View

Photo #2: Level 1 Variable Air Volume Box

Photo #3: Level 2 Electrical Pull Box

Photo #4: Level 2 Exterior Enclosure Progress

February 15 – February 19, 2021

Current Week Activities

- Elevator Core 1 – Stairs Levels 3-6 Concrete Pour
- Level 1 – Curtain Wall Glass Installation
- Level 1 – Mechanical, Electrical & Plumbing Risers
- Level 1 – Interior Priority Wall Framing
- Level 1 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 1 – Aerobics Room Operable Partition Support Steel
- Level 2 – Interior Priority Wall Framing
- Level 2 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 2 – Fan Coil Unit Installation
- Level 3 – Window Wall Sill Installation
- Site – Winter Weather Conditions

Upcoming Week Activities

- Elevator Core 1 – Level 13 Concrete Pour
- Level 7 – Concrete Balcony Pours
- Level 8 – Post-Tension Concrete Deck Pour #3
- Level 9 – Post-Tension Deck Framing
- Parking Level 1 – Mechanical, Electrical & Plumbing Rough-In
- Level 1 – Mechanical, Electrical & Plumbing Risers
- Level 1 – Interior Priority Wall Framing
- Level 1 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 2 – Interior Wall Framing
- Level 3 – Window Wall Installation
- Level 4 – Exterior Framing and Sheathing Panel Installation
- Site – Winter Weather Conditions

Upcoming Milestone/Major Dates

- Level 7 – Structure
- Level 8 – Structure
- Level 1 – Enclosure

Photo #1: Southeast Structure View

Photo #2: Level 1 Interior Wall Framing

Photo #3: Parking Level 1 Overhead Piping

Photo #4: Level 1 East Terrace Curtain Wall

February 8 – February 12, 2021

Current Week Activities

- Elevator Core 2 – Level 11 Concrete Pour
- Level 1 – Curtain Wall Glass Installation
- Level 1 – Mechanical, Electrical & Plumbing Risers
- Level 1 – Interior Priority Wall Framing
- Level 1 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 2 – Window Wall Installation
- Level 2 – Interior Priority Wall Framing
- Level 2 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 3 – Exterior Framing and Sheathing Panel Installation
- Level 7 – Concrete Balcony Pours
- Level 9 – Post-Tension Deck Framing
- Site – Winter Weather Conditions

Upcoming Week Activities

- Elevator Core 1 – Level 14 Concrete Pour
- Parking Level 1 – Mechanical, Electrical & Plumbing Rough-In
- Parking Level 1 – Air Handling Unit Delivery & Installation
- Level 1 – Mechanical, Electrical & Plumbing Risers
- Level 1 – Interior Priority Wall Framing
- Level 1 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 2 – Interior Priority Wall Framing
- Level 2 & 3 – Window Wall Installation
- Level 4 – Exterior Framing and Sheathing Panel Installation
- Level 8 – Post-Tension Concrete Deck Pour #3
- Site – Winter Weather Conditions

Upcoming Milestone/Major Dates

- Level 7 – Structure
- Level 8 – Structure
- Level 1 – Enclosure

Photo #1: Southeast Structure View

Photo #2: Site Chiller Installation

Photo #3: Level 2 Window Wall installation

Photo #4: Level 2 Shower Module Installation

February 1 – February 5, 2021

Current Week Activities

- Elevator Core 2 – Level 11 Concrete Pour
- Elevator Core 1 – Permanent Stair Concrete Pour
- Parking Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Curtain Wall Glass Installation
- Level 1 – Mechanical, Electrical & Plumbing Risers
- Level 2 – Interior Wall Top Track Installation
- Level 2 – Window Wall Installation
- Level 2 – Interior Mechanical Shaft Wall Installations
- Level 3 – Exterior Framing and Sheathing Panel Installation
- Level 7 – Concrete Balcony Pours
- Level 8 – Post-Tension Concrete Deck Pour #2

Upcoming Week Activities

- Elevator Core 1 – Level 13 Concrete Pour
- Elevator Core 2 – Permanent Stair Concrete Pour
- Parking Level 1 – Mechanical Piping & Ductwork Installation
- Parking Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Curtain Wall Glass Installation
- Level 1 – Mechanical, Electrical & Plumbing Risers
- Level 1 – Interior Priority Wall Framing
- Level 1 – Mechanical, Electrical & Plumbing In-Wall Rough-In
- Level 2 – Window Wall Installation
- Level 3 – Exterior Framing and Sheathing Panel Installation
- Level 7 – Concrete Balcony Pours
- Level 8 – Post-Tension Concrete Deck Pour #3

Upcoming Milestone/Major Dates

- Level 7 – Structure
- Level 8 – Structure
- Level 1 – Enclosure

Photo #1: Southeast Structure View

Photo #2: Level 1 Curtain Wall Glass Installation

Photo #3: Level 2 Permanent Stairs Pre-Pour

Photo #4: Parking Level 1 Area C Ductwork Installation

January 25 – January 29, 2021

Current Week Activities

- Elevator Core 1 – Level 12 Concrete Pour
- Elevator Core 2 – Permanent Stair Install
- Parking Level 1 – Mechanical Piping & Ductwork Installation
- Parking Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Curtain Wall Framing Installation
- Level 1 – Mechanical, Electrical & Plumbing Risers
- Level 1 – East Terrace Roofing Installation
- Level 2 – Window Wall Installation
- Level 7 – Concrete Balcony Pours
- Level 7 – Post-Tension Concrete Deck Pour #3
- Level 8 – Post-Tension Concrete Deck Pour #1

Upcoming Week Activities

- Elevator Core 2 – Level 11 Concrete Pour
- Elevator Core 2 – Permanent Stair Install
- Parking Level 1 – Mechanical Piping & Ductwork Installation
- Parking Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Curtain Wall Glass Installation
- Level 1 – Mechanical, Electrical & Plumbing Risers
- Level 1 – Interior Wall Top Track Installation
- Level 2 – Window Wall Installation
- Level 2 – Interior Wall Top Track Installation
- Level 3 – Exterior Framing and Sheathing Panel Installation
- Level 7 – Concrete Balcony Pours
- Level 8 – Post-Tension Concrete Deck Pour #2

Upcoming Milestone/Major Dates

- Level 7 – Structure
- Level 8 – Structure
- Level 1 – Enclosure

Photo #1: Southeast Structure View

Photo #2: Level 1 MEP Overhead Piping Installation

Photo #3: Parking Level 1 Area C Electrical Switch Gear Installation

Photo #4: Level 1 Prefabricated Bathroom Plumbing Assembly Installation

January 18 – January 22, 2021

Current Week Activities

- Elevator Core 1 – Level 11 Concrete Pour
- Elevator Core 1 – Permanent Stair Install
- Elevator Core 2 – Level 10 Concrete Pour
- Parking Level 1 – Ductwork Installation
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Curtain Wall Installation
- Level 2 – Exterior Pre-Fabricated Wall Panel Installation
- Level 2 – East Roofing Installation
- Level 6 – Concrete Balcony Pours
- Level 7 – Post-Tension Concrete Deck Formwork & Reinforcement
- Level 7 – Post-Tension Concrete Deck Pour #2
- Level 8 – Post-Tension Concrete Deck Formwork

Upcoming Week Activities

- Elevator Cores 1 & 2 – Reinforcement
- Elevator Core 2 – Permanent Stair Install
- Parking Level 1 – Ductwork Installation
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Curtain Wall Installation
- Level 1 – Mechanical, Electrical & Plumbing Risers
- Level 2 – Window Wall Installation
- Level 7 – Concrete Balcony Pours
- Level 7 – Post-Tension Concrete Deck Pour #3
- Level 8 – Post-Tension Concrete Deck Formwork & Reinforcement
- Level 8 – Post-Tension Concrete Deck Pour #1

Upcoming Milestone/Major Dates

- Level 6 – Structure
- Level 7 – Structure
- Level 1 – Enclosure

Photo #1: Southeast Structure View

Photo #2: Core #1 Permanent Stair Installation

Photo #3: Level 1 Area C Curtain Wall Installation

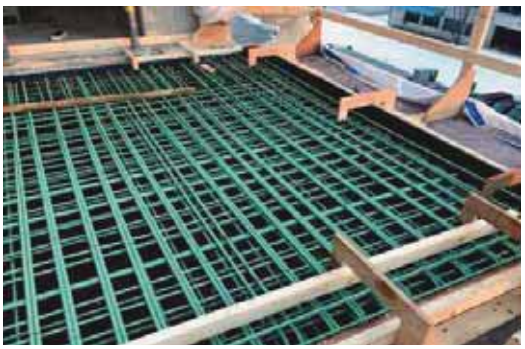

Photo #4: Level 6 Balcony Reinforcement Pre-Pour

January 11 – January 15, 2021

Current Week Activities

- Elevator Cores 1 & 2 – Reinforcement Installation
- Elevator Core 1 – Permanent Stair Install
- Parking Level 1 – Ductwork Installation
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Curtain Wall Installation
- Level 2 – Interior Wall Layout
- Level 2 – Exterior Pre-Fabricated Wall Panel Installation
- Level 6 – Post-Tension Concrete Deck Pour #3
- Level 6 – Concrete Balcony Pours
- Level 7 – Post-Tension Concrete Deck Formwork & Reinforcement
- Level 7 – Post-Tension Concrete Deck Pour #1

Upcoming Week Activities

- Elevator Core 2 – Level 10 Concrete Pour
- Elevator Core 1 – Permanent Stair Install
- Parking Level 1 – Ductwork Installation
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Curtain Wall Installation
- Level 2 – Exterior Pre-Fabricated Wall Panel Installation
- Level 2 – Window Wall Installation
- Level 6 – Concrete Balcony Pours
- Level 7 – Post-Tension Concrete Deck Formwork & Reinforcement
- Level 7 – Post-Tension Concrete Deck Pour #2

Upcoming Milestone/Major Dates

- Level 6 – Structure
- Level 7 – Structure
- Level 1 – Enclosure

Photo #1: Northwest Structure View

Photo #2: Level 7 Post-Tension Deck #1 Pre-Pour

Photo #3: Parking Level 1 Area C Interior Wall Installations

Photo #4: Parking Level 1 Area C Overhead MEP Installation

January 4 – January 8, 2021

Current Week Activities

- Elevator Cores 1 & 2 – Reinforcement
- Parking Level 1 – Interior CMU Partition Walls
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Exterior Framing & Sheathing Installation
- Level 2 – Roofing Installation
- Level 4 – Concrete Balcony Pours
- Level 5 – Post-Tension Concrete Deck Pour #3
- Level 5 – Concrete Balcony Pours
- Level 6 – Post-Tension Concrete Deck Forming & Reinforcement
- Site – Skip Hoist Installation up to Level 3

Upcoming Week Activities

- Elevator Core 2 – Level 9 Concrete Pour
- Parking Level 1 – Interior CMU Partition Walls
- Parking Level 1 – Mechanical Overhead Piping Installation
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Exterior Framing & Sheathing Installation
- Level 2 – Roofing Installation
- Level 5 – Concrete Balcony Pours
- Level 6 – Post-Tension Concrete Deck Reinforcement
- Level 6 – Post-Tension Concrete Deck Pour #1
- Site – Skip Hoist Loading Dock Installation

Upcoming Milestone/Major Dates

- Level 5 – Structure
- Level 6 – Structure

Photo #1: North Site Overview

Photo #2: Level 3 Elevator Core Slab Pre-Pour

Photo #3: Skip Hoist Delivery

Photo #4: South Structure View

December 14 – December 18, 2020

Current Week Activities

- Parking Level 1 – Interior CMU Partition Walls
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Exterior Framing & Sheathing Installation
- Level 1 – Air & Vapor Barrier Installation
- Level 1 – CMU Parapet Wall Installation
- Level 2 – Roofing Installation
- Level 4 – Concrete Balcony Pours
- Level 5 – Post-Tension Concrete Deck Pour #2
- Level 6 – Post-Tension Concrete Deck Forming
- Site – Permanent Chiller Concrete Pad Preparation

Upcoming Week Activities

- Elevator Cores 1 & 2 – Reinforcement
- Parking Level 1 – Interior CMU Partition Walls
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Exterior Framing & Sheathing Installation
- Level 2 – Roofing Installation
- Level 4 – Concrete Balcony Pours
- Level 5 – Post-Tension Concrete Deck Pour #3
- Level 5 – Concrete Balcony Pours
- Level 6 – Post-Tension Concrete Deck Forming & Reinforcement
- Site – Skip Hoist Installation

Upcoming Milestone/Major Dates

- Level 5 – Structure
- Level 6 – Structure

Photo #1: North Site Overview

Photo #2: Ground View of Structure Through Level 5

Photo #3: Level 2 Roofing Installation

Photo #4: Site Christmas Lighting

December 7 – December 11, 2020

Current Week Activities

- Elevator Core 1 Level 8 Concrete Pour
- Parking Level 1 – Interior CMU Partition Walls
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Exterior Framing & Sheathing Installation
- Level 1 – West Terrace Roofing Installation
- Level 2 – Roofing Preparations
- Level 4 – Post-Tension Concrete Deck Pour #3
- Level 4 – Concrete Balcony Pours
- Level 5 – Post-Tension Concrete Deck Forming & Reinforcement
- Level 5 – Post-Tension Concrete Deck Pour #1
- Permanent Chiller Underground Electrical & Mechanical Installation

Upcoming Week Activities

- Elevator Core 2 Level 8 Concrete Pour
- Parking Level 1 – Interior CMU Partition Walls
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Exterior Framing & Sheathing Installation
- Level 1 – West Terrace Roofing Installation
- Level 2 – Roofing Installation
- Level 4 – Concrete Balcony Pours
- Level 5 – Post-Tension Concrete Deck Forming & Reinforcement
- Level 5 – Post-Tension Concrete Deck Pour #2
- Permanent Chiller Underground Electrical & Mechanical Installation

Upcoming Milestone/Major Dates

- Level 5 – Structure
- Level 6 – Structure

Photo #1: North Site Overview

Photo #2: Level 4 Post-Tension Deck Pour #3 Reinforcement Detail

Photo #3: Level 1 Exterior Framing & Sheathing Installation

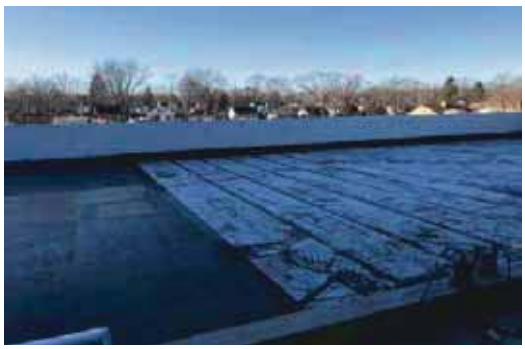

Photo #4: Level 1 Roofing Installation

November 30 – December 4, 2020

Current Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Interior CMU Partition Walls
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Area C Exterior CMU Parapet Wall
- Levels 1 & 2 – Concrete Curb Pours
- Level 2 – Roof Blocking
- Level 3 – Remaining Concrete Balcony Pours
- Level 4 – Post-Tension Concrete Deck Pour #2
- Level 5 – Post-Tension Concrete Deck Forming & Reinforcement
- Site - Permanent Chiller Pad Excavation

Upcoming Week Activities

- Elevator Cores 1 & 2 Level 7 Concrete Pour
- Parking Level 1 – Interior CMU Partition Walls
- Parking Level 1 – Exterior CMU Parapet Wall Air and Vapor Barrier
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Exterior Framing & Sheathing Installation
- Level 2 – Roofing Preparations
- Level 4 – Post-Tension Concrete Deck Pour #3
- Level 4 – Concrete Balcony Pours
- Level 5 – Post-Tension Concrete Deck Forming & Reinforcement
- Level 5 – Post-Tension Concrete Deck Pour #1
- Permanent Chiller Underground Electrical & Mechanical Installation

Upcoming Milestone/Major Dates

- Level 4 – Structure
- Level 5 – Structure

Photo #1: North Site Overview

Photo #2: Northeast View of Structure Through Level 5

Photo #3: Level 5 Decking

Photo #4: Level 1 Plumbing and Fire Protection Piping Installation

November 23 – November 27, 2020

Current Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Elevator Cores 1 & 2 Concrete Deck Pours
- Parking Level 1 – Area C Exterior CMU Walls
- Parking Level 1 – Temporary Water Meter Installation
- Parking Level 1 – Area B Exterior CMU Walls
- Parking Level 1 – Exterior Waterproofing
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Area C Exterior CMU Parapet Wall
- Levels 1 & 2 – Concrete Curb Pours
- Level 4 – Post-Tension Deck Forming & Reinforcement
- Level 4 – Concrete Column Pours
- Existing Chiller Demolition

Upcoming Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Interior CMU Partition Walls
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Area C Exterior CMU Parapet Wall
- Levels 1 & 2 – Concrete Curb Pours
- Levels 2 – Roofing Preparations
- Levels 3 – Remaining Concrete Balcony Pours
- Permanent Chiller Pad Preparations

Upcoming Milestone/Major Dates

- Level 4 – Structure
- Level 5 – Structure

Photo #1: North Site Overview

Photo #2: Level 4 Pre-Pour View

Photo #3: Parking Level 1 Area C CMU Exterior Enclosure Installation

Photo #4: Northeast Structure Through Level 4

November 16 – November 20, 2020

Current Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Elevator Cores 1 & 2 Level 7 Concrete Pour
- Parking Level 1 – Area C Exterior CMU Walls
- Parking Level 1 – Lintel Installation
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Levels 1 & 2 – Concrete Curb Pours
- Level 3 – Post-Tension Deck Pour # 3
- Level 3 – Concrete Column Pours
- Level 3 – Concrete Balcony Pours
- Level 4 – Post-Tension Deck Forming & Reinforcement
- Level 4 – Post-Tension Deck Pour #1

Upcoming Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Area C Exterior CMU Walls
- Parking Level 1 – Temporary Water Meter Installation
- PL1 & Level 1 – Electrical, Plumbing & Fire Protection Rough-In
- Level 1 – Area C Exterior CMU Parapet Wall
- Levels 1 & 2 – Concrete Curb Pours
- Level 4 – Post-Tension Deck Forming & Reinforcement
- Level 4 – Post-Tension Deck Pour #2
- Level 4 – Concrete Column Pours
- Existing Chiller Demolition

Upcoming Milestone/Major Dates

- Level 4 – Structure
- Level 5 – Structure

Photo #1: North Site Overview

Photo #2: Level 3 Balcony Reinforcement

Photo #3: Level 3 Post-Tension Deck Pour #3 Pre-Pour

Photo #4: Level 3 Post-Tension Deck Reinforcement Detail

November 9 – November 13, 2020

Current Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Parking Level 1 – Area C Exterior CMU Walls
- Parking Level 1 – Electrical Conduit Installation
- Level 1 – Fire Protection Hangers & Piping Installation
- Level 1 – Plumbing Hangers & Piping Installation
- Level 1 – Concrete Curb Pours
- Level 3 – Post-Tension Deck Forming & Reinforcement
- Level 3 – Post-Tension Deck Pour # 2
- Level 3 – Column Concrete Pours
- Level 4 – Post-Tension Deck Forming & Reinforcement

Upcoming Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Area C Exterior CMU Walls
- Parking Level 1 – Electrical Conduit Installation
- Parking Level 1 – Fire Protection Hangers & Piping Installation
- Level 1 – Plumbing Hangers & Piping Installation
- Level 1 – Concrete Curb Pours
- Level 3 – Post-Tension Deck Pour # 3
- Level 3 – Column Concrete Pours
- Level 4 – Post-Tension Deck Forming & Reinforcement
- Level 4 – Post-Tension Deck Pour #1

Upcoming Milestone/Major Dates

- Level 3 – Structure
- Level 4 – Structure

Photo #1: North Site Overview

Photo #2: Level 1 & 2 Structure View

Photo #3: Level 3 Post-Tension Deck Pour #2 Preparations

Photo #4: Building Area C CMU Walls

November 2 – November 6, 2020

Current Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Elevator Cores 1 & 2 Level 5 Concrete Pour
- Remaining Site Logistical Paving
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Parking Level 1 – Electrical Conduit Installation
- Parking Level 1 – Fire Protection Hangers & Piping Installation
- Parking Level 1 – Area C Exterior CMU Walls Preparation
- Level 1 – Plumbing Hangers & Piping Installation
- Level 1 – Curb Concrete Pours
- Level 3 – Post-Tension Deck Forming & Reinforcement
- Level 3 – Post-Tension Deck Pour # 1

Upcoming Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Parking Level 1 – Area C Exterior CMU Walls
- Parking Level 1 – Electrical Conduit Installation
- Parking Level 1 – Fire Protection Hangers & Piping Installation
- Level 1 – Plumbing Hangers & Piping Installation
- Level 1 – Curb Concrete Pours
- Level 3 – Post-Tension Deck Forming & Reinforcement
- Level 3 – Post-Tension Deck Pour # 2
- Level 3 – Column Concrete Pours

Upcoming Milestone/Major Dates

- Level 3 – Structure
- Level 4 – Structure

Photo #1: North Site Overview

Photo #2: Level 3 - Post-Tension Deck Pre-Pour

Photo #3: Parking Level 1 through Level 2 View

Photo #4: Level 1 - Concrete Curb Formwork

October 26 – October 30, 2020

Current Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Parking Level 1 – Area C Exterior CMU Walls
- Parking Level 1 – Electrical Conduit Installation
- Level 1 – Plumbing Hangers & Piping Installation
- Level 2 – Column Concrete Pours
- Level 2 – Post-Tension Deck Reinforcement
- Level 2 – Post-Tension Deck Pour #'s 6,7 & 8 – L2 Complete!
- Level 3 – Post-Tension Deck Forming & Reinforcement
- Temporary Chiller Installation

Upcoming Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Elevator Cores 1 & 2 Level 5 Concrete Pour
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Parking Level 1 – Area C Exterior CMU Walls
- Parking Level 1 – Electrical Conduit Installation
- Parking Level 1 – Fire Protection Hangers & Piping Installation
- Level 1 – Plumbing Hangers & Piping Installation
- Level 3 – Post-Tension Deck Forming & Reinforcement
- Level 3 – Post-Tension Deck Pour # 1

Upcoming Milestone/Major Dates

- Level 3 – Structure
- Level 4 – Structure

Photo #1: Northeast Site Overview

Photo #2: Parking Level 1 Electrical Conduit Installation

Photo #3: Level 2 Lockable Dowels Reinforcement Detail

Photo #4: Parking Level 1 Pool Area Post-Pour

Current Week Activities

- Monumental Stair Excavation
- Elevator Cores 1 & 2 Level 4 Concrete Pour
- Parking Level 2 – Fire Protection Hangers & Piping Installation
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Parking Level 1 – Natural Gas Piping Installation
- Level 2 – Column Concrete Pours
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Level 2 – Post-Tension Deck Pours #4 & 5
- Level 3 – Post-Tension Deck Forming
- West Site Berm Final Grading & Landscaping

Upcoming Week Activities

- Elevator Cores 1 & 2 Reinforcement
- Parking Level 2 – Fire Protection Hangers & Piping Installation
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Parking Level 1 – Area C Exterior CMU Walls
- Level 2 – Column Concrete Pours
- Level 2 – Post-Tension Deck Reinforcement
- Level 2 – Post-Tension Deck Pour #'s 6 & 7
- Level 3 – Post-Tension Deck Forming & Reinforcement
- South Site Grading and Logistics Paving Preparation
- West Site Berm Landscaping

Upcoming Milestone/Major Dates

- Level 2 – Structure
- Level 3 – Structure

Photo #1: Northwest Site Ground View

Photo #2: Elevator Core 1 Interior View

Photo #3: Parking Level 2 Fire Protection Piping Installation

Photo #4: West Site Berm Planting

Current Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Elevator Cores 1 & 2 Reinforcement for Level 3 Lift
- Parking Level 2 – Fire Protection Hangers & Piping Installation
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Level 2 – Column Concrete Pours
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Level 2 – Post-Tension Deck Pour #3
- Level 2 – Area B Balcony Concrete Pours
- South Site Grading and Logistics Paving Preparation

Upcoming Week Activities

- Foundation Wall Perimeter Backfill
- Elevator Cores 1 & 2 Reinforcement
- Parking Level 2 – Fire Protection Hangers & Piping Installation
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Level 2 – Column Concrete Pours
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Level 2 – Post-Tension Deck Pour #'s 4, 5 & 7
- Level 3 – Post-Tension Deck Forming
- South Site Grading and Logistics Paving Preparation
- West Site Berm Final Grading & Planting

Upcoming Milestone/Major Dates

- Level 2 – Structure
- Level 3 – Structure

Photo #1: North Site Overview

Photo #2: Southeast Site View

Photo #3: Parking Level 1-2 Ramp

Photo #4: Level 2 - Post-Tensioned Deck #3 Post-Pour

October 5 – October 9, 2020

Current Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Plumbing Hangers & Drain Piping Installation
- Parking Level 1 – Area B Stoop
- Level 1 – Column Concrete Pours
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Level 2 – Post-Tension Deck Pour #2
- West Site Logistics Grading & Paving Preparation
- WE Energies Transformer Installation

Upcoming Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Level 2 – Column Concrete Pours
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Level 2 – Post-Tension Deck Pour #3
- West Site Logistics Paving

Upcoming Milestone/Major Dates

- Level 2 – Structure
- Level 3 – Structure

Photo #1: Northeast Site Overview

Photo #2: Level 2 Pour #2 South View

Photo #3: WE Energies Transformer Installation

Photo #4: Level 2 Pour #2 Reinforcement

September 28 – October 2, 2020

Current Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Pool Area Backfill & Grading
- Parking Level 1 – Plumbing Hangers & Piping Installation
- Level 1 – Column Concrete Pours
- Level 1 – Post-Tension Deck Pour #8
- Level 2 – Post-Tension Deck Pour #1
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Elevator Core 1 – Level 2 Concrete Pour
- Elevator Core 2 – Level 3 Concrete Pour

Upcoming Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Elevator Cores 1 & 2 Reinforcement
- Parking Level 1 – Plumbing Hangers & Drain Piping Installation
- Level 1 – Column Concrete Pours
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Level 2 – Post-Tension Deck Pour #2
- Level 2 – Post-Tension Deck Pour #1 – Balconies
- Site Logistical Paving

Upcoming Milestone/Major Dates

- Level 2 – Structure
- Level 3 – Structure

Photo #1: Level 1 - Northeast Site Overview

Photo #2: Level 2 Post-Tension Deck

Photo #3: Level 2 Transfer Girder Reinforcement

Photo #4: Level 1 - Post-Tensioned Deck Pour #8 - Pre-Pour

September 21 – September 25, 2020

Current Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Pool Area Backfill & Grading
- Parking Level 1 – Plumbing Hangers & Drain Piping Installation
- Level 1 – Post-Tension Deck Pour #5
- Level 1 – Post-Tension Deck Pour #6
- Level 1 – Post-Tension Deck Pour #7
- Level 1 – Column Concrete Pours
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Site Retention Pond Excavation & Grading

Upcoming Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Elevator Cores 1 & 2 Reinforcement
- Elevator Cores 1 & 2 Interior Concrete Wall Pours & Backfill
- Parking Level 1 – Plumbing Hangers & Drain Piping Installation
- Level 1 – Column Concrete Pours
- Level 1 – Post-Tension Deck Pour #8
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Level 2 – Post-Tension Deck Pour #1
- West Site Grading

Upcoming Milestone/Major Dates

- Level 1 – Structure
- Level 2 – Structure

Photo #1: Level 1 - Northeast Site Overview

Photo #2: Pool Area Back Filling

Photo #3: Core Concrete Placing Boom Installation

Photo #4: Site Retaining Pond Grading

September 14 – September 18, 2020

Current Week Activities

- Foundation Wall Perimeter Backfill
- Parking Level 1 – Plumbing Hangers & Drain Piping Installation
- Elevator Cores 1 & 2 Up to Level 3
- Level 1 – Final Post-Tension Deck Forming
- Level 1 – Post-Tension Deck Reinforcement Pour #6
- Level 1 – Post-Tension Deck Reinforcement Pour #7
- Level 1 – Post-Tension Deck Reinforcement Pour #8
- Level 1 – Column Concrete Pours
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Site Retention Pond Excavation
- Final Mockup Functional Testing

Upcoming Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Elevator Cores 1 & 2 Reinforcement
- Level 1 – Column Concrete Pours
- Level 1 – Post-Tension Deck Pour #5
- Level 1 – Post-Tension Deck Pour #6
- Level 1 – Post-Tension Deck Pour #7
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Loading Dock Ramp & Retaining Walls Backfill

Upcoming Milestone/Major Dates

- Level 1 – Structure
- Level 2 – Structure

Photo #1: Level 1 - Final Post-Tension Deck Forming

Photo #2: Site Retention Pond Excavation

Photo #3: Level 1 - Beam Reinforcing

Photo #4: Level 1 - Post-Tension Deck Reinforcement Pour #6

September 8 – September 12, 2020

Current Week Activities

- Foundation Wall Perimeter Backfill
- Parking Level 1 – Plumbing Hangers & Drain Piping Installation
- Elevator Cores 1 & 2 Up to Level 3
- Level 1 – Final Post-Tension Deck Forming
- Level 1 – Post-Tension Deck Reinforcement
- Level 1 – Column Concrete Pours
- Level 1 – Post-Tension Deck Pour #5 Site Retaining Pond Excavation
- Site Underground Sanitary & Storm Line Installation
- Loading Dock Ramp & Retaining Walls Backfill and Grading

Upcoming Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Elevator Cores 1 & 2 Reinforcement
- Level 1 – Column Concrete Pours
- Level 1 – Post-Tension Deck Pour #5
- Level 1 – Post-Tension Deck Reinforcement
- Level 2 – Post-Tension Deck Forming & Reinforcement
- Parking Level 1 - Plumbing Hangers & Drain Piping Installation
- WE Energies Primary Power Underground

Upcoming Milestone/Major Dates

- Level 1 – Structure
- Level 2 – Structure

Photo #1: Northeast Site Overview

Photo #2: Retaining Pond Excavation

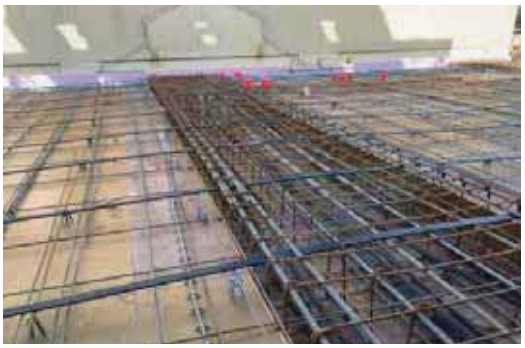

Photo #3: Level 01 PT Pour #5 Beam Reinforcement

Photo #4: Level 01 PT Pour #4

Current Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Parking Level 1 – Area C Slab-On-Grade
- Parking Level 1 – Area D Foundation Wall Pour
- Level 1 – Transfer Girder Installation
- Level 1 – Post-Tension Deck Forming & Reinforcem ent
- Level 1 – Column Concrete Pours
- Mockup Functional Testing
- Loading Dock Ramp Retaining Walls

Upcoming Week Activities

- Foundation Wall Perimeter Backfill
- Exterior Foundation Wall Waterproofing
- Level 1 – Elevator Cores 1 & 2 Up to Level 3
- Level 1 – Post-Tension Deck Forming & Reinforcement
- Level 1 – Column Concrete Pours
- Level 1 – Post-Tension Deck Pour #4
- Level 1 – Post-Tension Deck Pour #5
- Parking Level 1 – Area D Foundation Wall Pour
- Loading Dock Ramp Retaining Walls

Upcoming Milestone/Major Dates

- Level 1 – Structure
- Level 2 – Structure

Photo #1: Northeast Site Overview

Photo #2: Level 1 Transfer Girder

Photo #3: Parking Level 1 Slab-On-Grade #5 Preparation

Photo #4: Northwest Site Overview

Current Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Foundation Wall Waterproofing
- Parking Level 1 – Area D In-Ground Plumbing
- Parking Level 1 – Area D Slab-On-Grade
- Level 1 – Post-Tension Deck Forming and Reinforcement
- Level 1 – Pour Columns
- Level 1 – Post-Tension Pour #1
- Loading Dock Retaining Wall Foundation
- 103rd Street Berm & Northwest Pond Seeding
- Foundation Wall Perimeter Backfill
- Elevator #5 Concrete Slab and Walls

Upcoming Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Area C Slab-On-Grade
- Level 1 – Elevator Core 1 Up to Level 2
- Level 1 – Post-Tension Deck Forming & Reinforcement
- Level 1 – Post-Tension Deck Pour #3
- Level 1 – Post-Tension Deck Pour #4
- Level 2 – Elevator Core 1 Up to Level 3
- Parking Level 1 – Area D Foundation Wall Pour
- Foundation Wall Perimeter Backfill
- Loading Dock Ramp Retaining Walls

Upcoming Milestone/Major Dates

- Parking Level 1 – Slab-On-Grade
- Level 1 – Structure

Photo #1: Parking Level 1, Area D Vapor Barrier

Photo #2: Post-Tension Deck Shoring

Photo #3: Level 1, Post-Tension Deck Pour #2 Prep

Photo #4: Parking Level 2, Deck Reshoring

August 17 – 22, 2020

Current Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Foundation Wall Waterproofing
- Parking Level 1 – Area C Slab-On-Grade
- Parking Level 1 – Area D In-Ground Plumbing
- Parking Level 1 – Area D Foundation Walls
- Level 1 – Post-Tension Deck Forming and Reinforcement
- Loading Dock Ramp Excavation
- Northwest Parking Lot Asphalt Pavement
- San Camillo Kitchen Hood Fan Relocation
- 103rd Street Berm Grading

Upcoming Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Area C Slab-On-Grade
- Parking Level 1 – Area D Foundation Walls
- Level 1 – Elevator Core 1 Up to Level 2
- Level 1 – Post-Tension Deck Forming & Reinforcement
- Level 1 – Post-Tension Deck Pour #1
- Foundation Wall Perimeter Backfill
- Elevator #5 Concrete Slab and Walls
- Loading Dock Ramp Foundation Walls

Upcoming Milestone/Major Dates

- Parking Level 1 – Slab-On-Grade
- Level 1 – Structure

Photo #1: Northeast Site Overview

Photo #2: Level 1 Post-Tension Deck Shoring

Photo #3: Parking Level 1 Area C Slab-On-Grade

Photo #4: North Site Overview

Current Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Column Placement
- Parking Level 1 – Area B Slab-On-Grade
- Parking Level 1 – Area C Slab-On-Grade
- Parking Level 1 – Area D Foundation Walls
- Parking Level 1 – Area D In-Ground Plumbing
- Parking Level 1 – Foundation Wall Pours
- Level 1 – Post-Tension Deck Forming and Reinforcement
- Level 1 – Post-Tension Deck Pour #1

Upcoming Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Area C Slab-On-Grade
- Parking Level 1 – Area D Foundation Walls
- Parking Level 1 – Column Concrete Placement
- Level 1 – Elevator Core 2 Up to Level 2
- Level 1 – Post-Tension Deck Forming & Reinforcement
- Level 1 – Post-Tension Deck Pour #2
- Foundation Wall Perimeter Backfill
- Northwest Parking Lot Asphalt Pavement
- San Camillo Kitchen Hood Fan Relocation

Upcoming Milestone/Major Dates

- Parking Level 1 – Slab-On-Grade
- Level 1 – Structure

Photo #1: Northeast Site Overview

Photo #2: Level 1 Area B Post-Tension Deck

Photo #3: Parking Level 1 Area C Slab-On-Grade Preparation

Photo #4: Northwest Site Overview

Current Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Area B In-Ground Plumbing
- Parking Level 1 – Area C Backfill
- Parking Level 1 – Area D Footings and Columns
- Parking Level 1 – Area D Backfill
- Parking Level 1 – Column Concrete Placement
- Parking Level 1 – Foundation Wall Pours
- Parking Level 1 – Ramp Concrete Slab Pour
- Level 1 – Post-Tensioned Concrete Slab Form & Reinforcement
- San Camillo North Parking Lot Concrete Curb Installation
- West Side Parking Lot Grading and Preparation

Upcoming Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Area D Foundation Walls
- Parking Level 1 – Column Concrete Placement
- Parking Level 1 – Area B Foundation Walls
- Parking Level 1 – Area B Slab-On-Grade
- Level 1 – Post-Tensioned Concrete Slab Form & Reinforcement
- Level 1 – Post-Tensioned Concrete Slab Pour
- Foundation Wall Perimeter Backfill

Upcoming Milestone/Major Dates

- Parking Level 1 – Post-Tensioned Slab & Slab-On-Grade
- Level 1 – Post-Tensioned Slab

Photo #1: North-East Site Overview

Photo #2: Level 1 Post-Tensioned Deck Preperation

Photo #3: Parking Level 1 Area B Slab-On-Grade

Photo #4: Parking Level Ramp Concrete Slab-On-Grade

July 27 – July 31, 2020

Current Week Activities

- Excavation of Perimeter Foundation System
- Layout of Penetrations Through Concrete Walls / Foundations
- Foundation Wall Waterproofing
- Parking Level 1 – Area B In-Ground Plumbing
- Parking Level 1 – Area B Slab-On-Grade
- Parking Level 1 – Area C Footings and Columns
- Parking Level 1 – Area D Footings and Columns
- Parking Level 1 – Post-Tensioned Concrete Slab Rebar Placement
- Parking Level 1 – Pool Foundation Wall Pour
- Parking Level 1 – Post-Tensioned Concrete Pour #4
- Parking Level 1 – Foundation Wall Pours
- Level 1 – Post-Tensioned Concrete Slab Form Placement
- Main Electrical Service Rough-In

Upcoming Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Area D Foundation Walls
- Parking Level 1 – Area D Foundation
- Parking Level 1 – Column Concrete Placement
- Parking Level 1 – Area B Foundation Walls
- Parking Level Ramp Slab-On-Grade Preparation
- Foundation Wall Waterproofing

Upcoming Milestone/Major Dates

- Parking Level 2 – Ramp Slab-On-Grade
- Parking Level 1 – Post-Tensioned Slab & Slab-On-Grade
- Level 1 – Post-Tensioned Slab

Photo #1: North-East Site Overview

Photo #2: Parking Level 1 Area C Columns and Foundation Wall Form System

Photo #3: Parking Level 1 Post Tensioned Slab Pre-Pour

Photo #4: Pool Foundation Wall Reinforcement

July 20 – July 24, 2020

Current Week Activities

- Excavation of Perimeter Foundation System
- Layout of Penetrations Through Concrete Walls / Foundations
- Foundation Wall Waterproofing
- Parking Level 1 – Area B Columns Concrete Placement
- Parking Level 1 – Area D Excavation of Perimeter Foundation System
- Parking Level 1 – Post-Tensioned Concrete Slab Form Placement
- Parking Level 1 – Post-Tensioned Concrete Slab Rebar Placement
- Area C Footings and Columns
- Main Electrical Service Rough-In
- Mock-Up – Function Testing & Exterior Veneer Installed
- North San Camillo Parking Lot Closure and Paving

Upcoming Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Area D Excavation of Perimeter Foundation System
- Parking Level 1 – Column Concrete Placement
- Parking Level 1 – Area B Foundation Walls
- Parking Level 1 – Post-Tensioned Concrete Slab Decking
- Parking Level 1 – Post-Tensioned Concrete Pour #3
- Parking Level Ramp Slab-On-Grade Preparation
- Foundation Wall Waterproofing
- Mock-Up Coordination

Upcoming Milestone/Major Dates

- Parking Level 2 – Ramp Slab-On-Grade
- Parking Level 1 – Post-Tensioned Slab & Slab-On-Grade

Photo #1: North-East Site Overview

Photo #2: Parking Level 1 Area C Overview

Photo #3: 3 Hour Rated Concrete Masonry Unit Wall

Photo #4: Mock-Up Progress

Current Week Activities

- Excavation of Perimeter Foundation System
- Layout of Penetrations Through Concrete Walls / Foundations
- Foundation Wall Waterproofing
- Parking Level 1 – Area B Columns Concrete Placement
- Parking Level 1 – Area D Excavation of Perimeter Foundation System
- Parking Level 1 – Post-Tensioned Concrete Slab Form Placement
- Parking Level 1 – Post-Tensioned Concrete Slab Rebar Placement
- Main Electrical Service Rough-In
- 3-hour Concrete Masonry Unit Fire Wall
- Mock-Up – Window Wall Installation

Upcoming Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Area D Excavation of Perimeter Foundation System
- Parking Level 1 – Column Concrete Placement
- Parking Level 1 – Area B Foundation Walls
- Parking Level 1 – Post-Tensioned Concrete Slab Decking
- Parking Level 1 – Post-Tensioned Concrete Pour #2
- Parking Level Ramp Slab-On-Grade Preparation
- Foundation Wall Waterproofing
- 16-inch CMU Foundation Wall
- Mock-Up – Function Testing Procedures
- North San Camillo Parking Lot Closure and Paving

Upcoming Milestone/Major Dates

- Parking Level 2 – Ramp Slab-On-Grade
- Parking Level 1 – Post-Tensioned Slab & Slab-On-Grade

Photo #1: North-East Site Overview

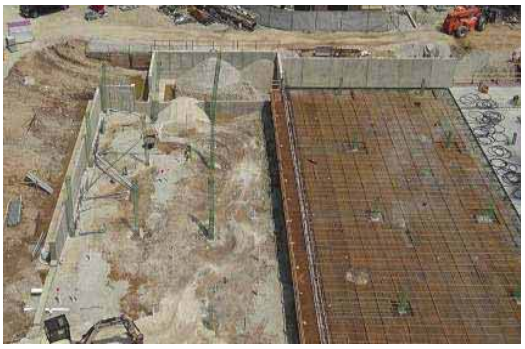

Photo #2: Parking Level 1 Area C Overview

Photo #3: Parking Level 2

Photo #4: Parking Level 1 Area B/C

Current Week Activities

- Excavation of Perimeter Foundation System
- Concrete Placement of Parking Level 1 Pile Caps
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Layout of Penetrations Through Concrete Walls / Foundations
- Foundation Wall Waterproofing
- Parking Level 1 – Area B Piled Spread Footings
- Parking Level 1 – Post-Tensioned Concrete Slab Form Placement
- Parking Level 1 – Post-Tensioned Concrete Slab Rebar Placement
- Parking Level 1 – Post-Tensioned Concrete Pour #1
- Parking Levels 2 to 1 Ramp Excavation
- Main Electrical Service Rough-In
- 3-hour Concrete Masonry Unit Fire Wall
- Mock-Up – Window Wall & Curtain Wall Installation

Upcoming Week Activities

- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Area D Excavation of Perimeter Foundation System
- Parking Level 1 – Column Concrete Placement
- Parking Level 1 – Area B Foundation Walls
- Parking Level 1 – Post-Tensioned Concrete Slab Decking
- Parking Level 1 – Post-Tensioned Concrete Pour #2
- Foundation Wall Waterproofing
- 3-hour Concrete Masonry Unit Fire Wall
- Mock-Up – Window Wall & Curtain Wall Installation

Upcoming Milestone/Major Dates

- Parking Level 2 – Ramp Slab-On-Grade
- Parking Level 1 – Post-Tensioned Slab & Slab-On-Grade

Photo #1: North-East Site Overview

Photo #2: North Site Overview

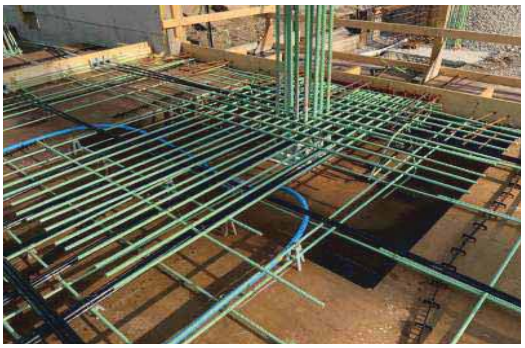

Photo #3: Parking Level 1 - Column Rebar - Before Concrete Pour

Photo #4: 3-Hour Concrete Masonry Unit Wall

June 29 – July 3, 2020

Current Week Activities

- Excavation of Perimeter Foundation System
- Concrete Placement of Parking Level 1 Pile Caps & Columns
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Layout of Penetrations Through Concrete Walls / Foundations
- Foundation Wall Waterproofing
- Parking Level 1 – Area B & C Piled Spread Footings
- Parking Level 1 – Post-Tensioned Concrete Slab Form Placement
- Parking Level 1 – Post-Tensioned Concrete Slab Rebar Placement
- Parking Levels 1 to 2 Ramp Excavation
- Parking Level 2 – Slab on Grade Concrete Placement
- Berm Segmented Block Retaining Wall
- Main Electrical Service Rough-In
- Mock-Up – Window Wall & Curtain Wall Installation
- Core 1 – Concrete Pour up to Level 1

Upcoming Week Activities

- Excavation of Perimeter Foundation System
- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Column Concrete Placement
- Parking Level 1 – Area B Foundation Walls
- Parking Level 1 – Post-Tensioned Concrete Slab Form Placement
- Parking Level 1 – Post-Tensioned Concrete Pour #1
- Foundation Wall Waterproofing
- 3-hour Concrete Masonry Unit Fire Wall
- Mock-Up – Window Wall & Curtain Wall Installation

Upcoming Milestone/Major Dates

- Parking Level 1 – Post-Tensioned Slab & Slab On Grade — June 22 - 26, 2020

Photo #1: North-East Site Overview

Photo #2: Foundation Wall Waterproofing Installation

Photo #3: Parking Level 1 Area C - Walls and Column Rebar

Photo #4: West Side Retaining Wall

Current Week Activities

- Excavation of Perimeter Foundation System
- Concrete Placement of Parking Level 1 Pile Caps & Columns
- Core 2 – Concrete Pour up to Level 1
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Layout of Penetrations Through Concrete Walls / Foundations
- Foundation Wall Waterproofing
- Parking Level 1 – Area B & C Piled Spread Footings
- Parking Level 1 – Post-Tensioned Concrete Slab Form Placement
- Parking Level 2 – Set Floor Drains
- Parking Level 2 – Slab on Grade Concrete Placement
- Berm Segmented Block Retaining Wall
- Main Electrical Service Rough-In
- Mock-Up - Exterior Sheathing & Air and Vapor Barrier

Upcoming Week Activities

- Excavation of Perimeter Foundation System
- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Pile Caps & Columns Concrete Placement
- Parking Level 1 – Area B & C Piled Spread Footings
- Parking Level 1 – Area B & C Foundation Walls
- Core 1 – Concrete Pour up to Level 1
- Berm Segmented Block Retaining Wall
- 3-hour Concrete Masonry Unit Fire Wall
- Parking Level 1 – Post-Tensioned Concrete Slab Form Placement

Upcoming Milestone/Major Dates

- Parking Level 1 – Post-Tensioned Slab

Photo #1: North-East View

Photo #2: Parking Level 2 Slab On Grade Concrete Pour

Photo #3: Window Wall Mock-Up

Photo #4: Parking Level 2 South-West View

June 15 - 19, 2020

Current Week Activities

- Excavation of Perimeter Foundation System
- Concrete Placement of Parking Level 1 Pile Caps & Columns
- Core 2 Hydraulic Self-Climbing Form System Installation
- Core 2 Concrete Pour, Lift 3
- Install Stone Sub-Base, Parking Level 2
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Layout of Penetrations Through Concrete Walls / Foundations
- Foundation Wall Waterproofing
- Parking Level 1, Area C Piled Spread Footings
- Berm Segmented Block Retaining Wall
- Main Electrical Service Rough-In

Upcoming Week Activities

- Excavation of Perimeter Foundation System
- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1 – Pile Caps & Columns Concrete Placement
- Parking Level 1 – Area C Piled Spread Footings
- Parking Level 1 – Area C Foundation Walls
- Parking Level 2 – Slab on Grade Preparation
- Parking Level 2– Slab on Grade, Pour 1
- Parking Level 2 – Set Floor Drains
- Core 2 Concrete Pour, Lift 3
- Berm Segmented Block Retaining Wall
- Grade East One Way Drive Lane

Upcoming Milestone/Major Dates

- Parking Level 2 – Slab on Grade

Photo #1: Site Overview - East

Photo #2: Parking Level 2 Underground Conduit

Photo #3: Parking Level Ramp Water Proofing

Photo #4: Parking Level 2 Slab On Grade Final Grading

June 8 - 12, 2020

Current Week Activities

- Excavation of Perimeter Foundation System
- Concrete Placement of Pile Caps & Columns
- Foundation Wall Tie-In to Elevator Core 2
- Core 2 Hydraulic Self-Climbing Form System Installation
- Core 2 Concrete Pour, Lift 3
- Install Stone Sub-Base, Parking Level 2
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Layout of Penetrations Through Concrete Walls / Foundations
- Core 1, 2 & 3 Perimeter Waterproofing
- Parking Level 1, Area C Mat Slabs
- Main Electrical Service Rough-In

Upcoming Week Activities

- Excavation of Perimeter Foundation System
- Concrete Placement of Pile Caps & Columns
- Install Stone Sub-Base, Parking Level 2
- Layout of Penetrations Through Concrete Walls / Foundations
- Parking Level 1, Area C Mat Slabs
- Grade East One Way Drive Lane
- Parking Level 2 Slab on Grade Preparation
- Core 1 Lift 3
- Core 2 Lift 3
- Berm Segmented Block Retaining Wall

Upcoming Milestone/Major Dates

- Parking Level 2 – Slab on Grade

Photo #1: Site Overview - East

Photo #2: Foundation Wall Pour

Photo #3: Parking Level 2 Foundation

Photo #4: Core 1 Waterproofing and Backfill

Current Week Activities

- Excavation of Perimeter Foundation System
- Concrete Placement of Pile Caps & Columns
- Foundation Wall Concrete Pours 18 & 19
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Temporary Pavement East Side of South San Camillo Parking Lot
- Layout of Penetrations Through Concrete Walls / Foundations
- Site Utility Installation – Water to Gilligan's Island
- Core 2 Foundation Wall Concrete Pour, Lift 2
- Parking Level 1 Perimeter Foundation System Excavation

Upcoming Week Activities

- Excavation of Perimeter Foundation System
- Concrete Placement of Pile Caps & Columns
- Foundation Wall Tie-In to Elevator Core 2
- Core 2 Hydraulic Self-Climbing Form System Installation
- Core 2 Foundation Wall Concrete Pour, Lift 3
- Install Stone Sub-Base, Parking Level 2
- Grade East One Way Drive Lane
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Layout of Penetrations Through Concrete Walls / Foundations
- Core 1 Perimeter Waterproofing
- Parking Level 1 Area C Piled Spread Footings

Upcoming Milestone/Major Dates

- Parking Level 2 – Slab on Grade

Photo #1: Site Overview - East

Photo #2: Pile Cap Forming

Photo #3: Core 2 Lift 2 Concrete Pour

Photo #4: Parking Level 2 View

May 26 – May 29, 2020

Current Week Activities

- Excavation of Perimeter Foundation System
- Concrete Placement of Pile Caps
- Foundation Wall Concrete Pours 15 & 16
- Continue Placement of Mud Sills – Perimeter Wall System / Foundations
- Grade East Side of South San Camillo Parking Lot
- Layout of Penetrations Through Concrete Walls / Foundations
- Excavation & Install of Underground Chiller Piping
- Chiller Piping Pressure Testing
- Core 2 Foundation Wall Concrete Pour, Lift 1
- Site Utility Installation – Storm to Gilligan's Island
- Core 3 Perimeter Waterproofing
- Core 3 Piled Mat Concrete Pour

Upcoming Week Activities

- Continue Excavation of Perimeter Foundation System
- Continue Concrete Placement of Pile Caps
- Foundation Wall Concrete Pours 17, 18 & 19
- Continue Placement of Mud Sills – Perimeter Wall System / Foundations
- Temporary Pavement East Side of South San Camillo Parking Lot
- Continue Layout of Penetrations Through Concrete Walls / Foundations
- Site Utility Installation – Water to Gilligan's Island
- Core 2 Foundation Wall Concrete Pour, Lift 2

Upcoming Milestone/Major Dates

- Parking Level 2 – Slab on Grade

Photo #1: Bird's Eye View

Photo #2: Parking Level 2 Overview

Photo #3: Site Security Cameras

Photo #4: Chilled Water Piping Pressure Test

Current Week Activities

- Continue Excavation of Perimeter Foundation System
- Continue Concrete Placement of Pile Caps
- Foundation Wall Concrete Pours 8, 9 & 14
- Continue Placement of Mud Sills – Perimeter Wall System / Foundations
- Cut Down Pile Over-Runs
- Continue Layout of Penetrations Through Concrete Walls / Foundations
- Excavation & Install of Underground Chiller Piping
- Core 3 Perimeter Waterproofing
- Continue Underground Site Utility Installation – Sanitary & Storm
- Core 1 Underground Power
- Parking Level 2 Underground Plumbing

Upcoming Week Activities

- Continue Excavation of Perimeter Foundation System
- Continue Concrete Placement of Pile Caps
- Foundation Wall Concrete Pours 15 & 16
- Continue Placement of Mud Sills – Perimeter Wall System / Foundations
- Grade East Side of South San Camillo Parking Lot
- Continue Layout of Penetrations Through Concrete Walls / Foundations
- Continue Excavation & Install of Underground Chiller Piping
- Core 2 Foundation Wall Concrete Pour, Lift 1
- Continue Core 3 Perimeter Waterproofing
- Underground Site Utility Installation – Sanitary & Storm to Gilligan's Island

Upcoming Milestone/Major Dates

- Parking Level 2 – Slab on Grade

Photo #1: Core 3 Pile Mat

Photo #2: Core 1 DokaFlex Core Climber

Photo #3: Parking Level 2 Pile Mat & Caps

Photo #4: Foundation Wall Pours 8 & 9

May 11 – May 16, 2020

Current Week Activities

- Continue Excavation of Perimeter Foundation System
- Continue Concrete Placement of Pile Caps
- Foundation Wall Concrete Pours 5 & 6
- Continue Placement of Mud Sills – Perimeter Wall System / Foundations
- Core 2 Perimeter Waterproofing
- Pour Core 2 Concrete Piled Mat & Reinforcing Steel Install
- Cut Down Pile Over-Runs
- Continue Layout of Penetrations Through Concrete Walls / Foundations
- East Drive Closure
- Start Install of New Wauwatosa Water Main

Upcoming Week Activities

- Continue Excavation of Perimeter Foundation System
- Continue Concrete Placement of Pile Caps
- Foundation Wall Concrete Pours 8 & 9
- Continue Placement of Mud Sills – Perimeter Wall System / Foundations
- Cut Down Pile Over-Runs
- Continue Layout of Penetrations Through Concrete Walls / Foundations
- Excavation & Install of Underground Chiller Piping
- Core 1 – Foundation Wall Concrete Pour, Lift 2
- Core 3 Perimeter Waterproofing
- Continue Underground Site Utility Installation – Sanitary & Storm
- Demo Old Milwaukee Water Main & Meter Pit

Upcoming Milestone/Major Dates

- Parking Level 2 – Slab on Grade

Photo #1: Foundation Wall Concrete Pours 3 - 5

Photo #2: Mud Sill for Foundation Wall Concrete Pours 8 & 9

Photo #3: Elevator Core 2 Waterproofing Detailing

Photo #4: Southwest Parking Level 2 Overview

May 4 – May 9, 2020

Current Week Activities

- Continue Excavation of Perimeter Foundation System
- Continue South Site Utilities – Storm Trap
- Continue Concrete Placement of Pile Caps
- Foundation Wall Concrete Pours 3 & 4
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Cut Down Pile Over-Runs
- Continue Layout of Penetrations Through Concrete Walls / Foundations
- Start Core 1 Vertical Structure Forming & Reinforcing
- Concrete Pour Core 1 – Lift 1

Upcoming Week Activities

- Continue Excavation of Perimeter Foundation System
- Continue Concrete Placement of Pile Caps
- Foundation Wall Concrete Pours 5 - 7
- Continue Placement of Mud Sills – Perimeter Wall System / Foundations
- Core 2 Perimeter Waterproofing
- Concrete Pour Core 2 Piled Mat & Reinforcing Steel Install
- Cut Down Pile Over-Runs
- Continue Layout of Penetrations Through Concrete Walls / Foundations
- East Drive Closure
- Demo Old Milwaukee Water Main & Meter Pit
- Install New Chiller Piping
- Start Install of New Wauwatosa Water Main

Upcoming Milestone/Major Dates

- Parking Level 2 – Slab on Grade

Photo #1: Site Overview - Southwest

Photo #2: Foundation Wall Pours 1 & 2 Complete

Photo #3: Storm Trap

Photo #4: Foundation Wall Reinforcing Steel

April 27 – May 2, 2020

Current Week Activities

- Continue Excavation of Perimeter Foundation System
- South Site Utilities – Storm Trap Concrete Pad
- Continue Concrete Placement of Pile Caps
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Core #1 Perimeter Waterproofing
- Pour Core #1 Piled Mat & Start Core Wall Install
- Cut Down Pile Over-Runs
- Start Core #2 – Mud Slab & Perimeter Waterproofing
- Demobilize Pile Driving Cranes
- Start Layout of Penetrations Through Concrete
- Start Layout of Foundation Wall Sleeves

Upcoming Week Activities

- Continue Excavation of Perimeter Foundation System
- Continue South Site Utilities – Storm Trap
- Continue Concrete Placement of Pile Caps & Foundation Walls
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Core #2 Perimeter Waterproofing
- Pour Core #2 Piled Mat & Reinforcing Steel Install
- Cut Down Pile Over-Runs
- Continue Layout of Penetrations Through Concrete Walls / Foundations
- Start Core #1 Vertical Structure Forming & Reinforcing

Upcoming Milestone/Major Dates

- Parking Level 2 – Slab on Grade

Photo #1: Elevator Core #2

Photo #2: Foundation Wall Pour

Photo #3: Storm Trap Concrete Pad

Photo #4: Elevator Core #1

April 20 – April 25, 2020

Current Week Activities

- Continue Excavation of Perimeter Foundation System
- Finished Production Pile Installation
- Finished Excavation of Northwest Pond & Clay Liner
- South Site Utilities – Water Main & Grease Trap
- Continue Concrete Placement of Pile Caps
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Cut Down Pile Over-Runs
- Continue Excavation for Drilled Pier Caps

Upcoming Week Activities

- Continue Excavation of Perimeter Foundation System
- South Site Utilities – Storm Trap
- Continue Concrete Placement of Pile Caps
- Placement of Mud Sills – Perimeter Wall System / Foundations
- Core #1 Perimeter Waterproofing
- Pour Core #1 Piled Mat & Start Core Wall Install
- Cut Down Pile Over-Runs
- Start Core #2 – Mud Slab & Perimeter Waterproofing
- Demobilize Pile Driving Cranes
- Start Layout of Penetrations Through Concrete
- Start Layout of Foundation Wall Sleeves

Upcoming Milestone/Major Dates

- Deep Foundations – Complete

Photo #1: Site Foundation Overview

Photo #2: South Concrete Foundation

Photo #3: Final Piles Driven

Photo #4: Excavation for Drilled Pier Caps

Percentage of Piles Driven: **100% | 771 / 771 Piles – Pile Driving Complete!** April 13 – April 18, 2020

Current Week Activities

- **Tower Crane Lighting**
- **Continue Excavation for Perimeter Foundation System**
- Continue Excavation for D**rill Pile Caps**
- **Continue Production Pile Installation**
- **Cut Down Pile Over-Runs**
- **Continue Excavation of Northwest Pond & Clay Liner**
- **Set Parking Level 2 Sanitary & Storm Sump Crock**
- **First Pile Cap Concrete Pour**
- **Repair Diesel Hammer**
- **Start Pile Cap Rebar Installation**

Upcoming Week Activities

- **Continue** Excavation **for Perimeter FoundationSystem**
- Continue Excavation for D**rill Pile Caps**
- **Continue Production Pile Installation**
- **Finish Excavation of Northwest Pond & Clay Liner**
- **South Site Utilities – Water Main, Grease Trap, Storm Trap**
- **Continue Concrete Placement of Pile Caps**
- **Start Placement of Mud Sills – Perimeter Wall System / Foundations**
- **Start Foundation & Layout of Core #1**
- **Cut Down Pile Over-Runs**
- **Foundation Water Proofing**

Upcoming Milestone/Major Dates

- **Deep Foundations**

Photo #1: Parking Level 2 - Production Piles

Photo #2: Elevator Core Pile Installation

Photo #3: Pile Cap Rebar Installation Laydown Area

Photo #4: Pile Cap - West Side

Percentage of Piles Driven: 89% | 688 / 771 Piles

April 6 – April 11, 2020

Current Week Activities

- Continue Production Pile Installation
- Southeast Utility Installation
- Excavation of Northwest Pond
- Continue Mobilization for Starting Concrete Operations
- Temporary Power Underground to Tower Crane
- East Drive Closure – Tower Crane
- Tower Crane Assembly
- Excavate Core #1 & Install Lagging
- Start Foundation System Excavation – Walls / Caps
- Cut Down Pile Over-Cuts

Upcoming Week Activities

- Tower Crane Security
- Set Sump Pit
- Tower Crane Lighting
- Start Digging for Perimeter Foundation System & Drill Pile Caps
- Continue Production Pile Installation
- Continue Excavate Core #1 & Install Lagging
- Start Foundation System Excavation – Walls / Caps
- Cut Down Pile Over-Cuts
- Continue Mobilization for Starting Concrete Operations
- Excavation of Northwest Pond

Upcoming Milestone/Major Dates

- Deep Foundations

Photo #1: Crane Day

Photo #2: North Site - Production Pile Overview

Photo #3: Tower Crane Enclosure

Photo #4: Tower Crane Mast Assembly

Percentage of Piles Driven: 74% | 573 / 771 Piles

March 30 – April 4, 2020

Current Week Activities

- Continue Production Pile Installation
- Southeast Parking Lot Closure
- Southeast Utility Installation
- Roof Drain Mockups
- Start Excavation of Northwest Pond
- Continue Mobilization for Starting Concrete Operations
- Set Tower Crane Base Section & Pour Tower Crane Foundation
- Temporary Power Underground to Tower Crane
- Radiant Ceiling Panel Mockup

Upcoming Week Activities

- Continue Production Pile Installation
- Southeast Utility Installation
- Excavation of Northwest Pond
- Continue Mobilization for Starting Concrete Operations
- Temporary Power Underground to Tower Crane
- East Drive Closure – Tower Crane
- Tower Crane Assembly
- Excavate Core #1 & Install Lagging
- Start Foundation System Excavation – Walls / Caps
- Cut Down Pile Over-Cuts

Upcoming Milestone/Major Dates

- Deep Foundations

Percentage of Piles Driven: 57% | 443 / 771 Piles

Photo #1: North Site Overview

Photo #2: South End of Site - Piles

Photo #3: Production Pile Cranes

Photo #4: Southeast Parking Lot Closure for Utility Installation

March 23 – March 28, 2020

Current Week Activities

- Continue Production Pile Layout & Installation
- Mass Excavation – Parking Level 1, Areas C & D
- Finish Lagging Installation
- Continue Stone Placement – Parking Level 1
- Pour Tower Crane Concrete Foundation Installation
- Pour Pile Caps East of Tower Crane
- Start Site Utilities South of San Camillo
- Mobilize for Concrete Operations
- Continue Site Prep & Construction of Haul Road
- Implemented COVID-19 policies and procedures

Upcoming Week Activities

- Continue Production Pile Installation
- Southeast Parking Lot Closure
- Southeast Utility Installation
- Roof Drain Mockups
- Excavation of Northwest Pond
- Continue Mobilization for Starting Concrete Operations
- Set Tower Crane Base Section & Pour Tower Crane Foundation
- Temporary Power Underground to Tower Crane
- Radiant Ceiling Panel Mockup

Upcoming Milestone/Major Dates

- Mass Excavation Complete
- Deep Foundations

Photo #1: Southwest Production Piles

Photo #2: Site Aerial

Photo #3: Production Pile Layout & Installation

Photo #4: Complete Lagging Installation

Percentage of Piles Driven: 37% | 286 / 771 Piles

March 16 – March 21, 2020

Current Week Activities

- Sanitary Utility North of San Camillo
- Mass Excavation
- Production Pile Layout
- Start Production Pile Install
- Continue Lagging Install
- Start Stone Placement – Parking Levels 1 & 2
- Drain Tile Install – Parking Level 2
- Tower Crane Pad Pile Install
- Mobilize to South Side of Site for Starting Site Utilities

Upcoming Week Activities

- Continue Production Pile Layout & Installation
- Mass Excavation – Parking Level 1, Areas C & D
- Finish Lagging Installation
- Continue Stone Placement – Parking Level 1
- Pour Tower Crane Concrete Foundation Installation
- Pour Pile Caps East of Tower Crane
- Start Site Utilities South of San Camillo
- Mobilize for Concrete Operations
- Continue Site Prep & Construction of Haul Road

Upcoming Milestone/Major Dates

- Mass Excavation Complete
- Deep Foundations

Photo #1: Production Pile Cranes

Photo #2: Continued Lagging Installation: Northeast Corner

Photo #3: Tower Crane Pad Pile Install

Photo #4: Sanitary Utility North of San Camillo

Percentage of Piles Driven: 15% | 118 / 771 Piles

March 9 – March 14, 2020

Current Week Activities

- Production Pile Crane Assembly
- Production Pile Deliveries
- Testing Earth Retention System Tie Backs
- Under Cut Unsuitable Soils Parking Level 2
- Stone Installation Parking Level 2
- Start Underground Drain Tile
- Mass Excavation
- Tower Crane Layout & Foundation
- San Camillo Garage 1 & 2 Closure
- Storm Installation North of San Camillo

Upcoming Week Activities

- Sanitary Utility North of San Camillo
- Mass Excavation
- Production Pile Layout
- Start Production Pile Install
- Finish Lagging Install
- Stone Placement – Parking Levels 1 & 2
- Drain Tile Install – Parking Level 2
- Tower Crane Pad Pile Install
- Mobilize to South Side of Site for Starting Site Utilities

Upcoming Milestone/Major Dates

- Mass Excavation Complete
- Deep Foundations

Photo #1: Stone Parking Level 2

Photo #2: Court East Mass Excavation

Photo #3: Pile Crane Build

Photo #4: Storm North of San Camillo

March 2 – March 7, 2020

Current Week Activities

- Earth Retention System Pile Install & Lagging
- Install Earth Retention System Tie Backs
- Test Earth Retention System Tie Backs
- Earth Retention System Backfill
- Court West Soil Backfill
- Bid Release 05 Scope Reviews
- Excavate for Earth Retention System Lagging
- AT&T Fiber Re-Location Pathway
- Excavate for West Dry Stormwater Basin

Upcoming Week Activities

- Production Pile Crane Assembly
- Production Pile Deliveries
- Testing Earth Retention System Tie Backs
- Under Cut Unsuitable Soils Parking Level 2
- Stone Installation Parking Level 2
- Start Underground Drain Tile
- Mass Excavation
- Tower Crane Layout & Foundation
- San Camillo Garage 1 & 2 Closure
- Storm Installation North of San Camillo

Upcoming Milestone/Major Dates

- Mass Excavation Complete
- Deep Foundations

Photo #1: Earth Retention System-1 Lagging

Photo #2: Court West Soil Backfill

Photo #3: Earth Retention System-1 Overview

Photo #4: Earth Retention System-2 Pile Install

Current Week Activities

- Earth Retention System Pile Install & Lagging
- Continue Earth Retention System Bench Cut
- Install Earth Retention System Tie Backs
- Earth Retention System Backfill
- Court West Soil Backfill
- Backfill Environmental Undercuts on North East side of Side
- Storm in NW Parking Lot
- Bid Release 05 Scope Reviews
- Install Ramp for Mass Excavation

Upcoming Week Activities

- Earth Retention System Pile Install & Lagging
- Install Earth Retention System Tie Backs
- Test Earth Retention System Tie Backs
- Earth Retention System Backfill
- Court West Soil Backfill
- Bid Release 05 Scope Reviews
- Excavate for Earth Retention System Lagging
- AT&T Fiber Re-Location Pathway
- Excavate for West Dry Stormwater Basin

Upcoming Milestone/Major Dates

- Mass Excavation Complete
- Deep Foundations

Photo #1: Earth Retention System Lagging

Photo #2: Earth Retention System Pile Install

Photo #3: Earth Retention System Overview

Photo #4: Court West Soil Backfill

February 17 - February 22, 2020

Current Week Activities

- Finish Court East Demo & Remove Foundations
- Start Earth Retention System Pile Install
- Earth Retention System Bench Cut
- Court West Soil Backfill
- Finish Sanitary Main – NW Site – North Main
- Berm Placement – 103rd St.
- Continue Rough / Framing / Grading NW Parking Lot
- Start Storm Tie-In by Kathy's House

Upcoming Week Activities

- Earth Retention System Pile Install & Lagging
- Continue Earth Retention System Bench Cut
- Earth Retention System Tie Backs
- Earth Retention System Backfill
- Court West Soil Backfill
- Backfill Environmental Undercuts on North East side of Side
- Storm in NW Parking Lot
- Bid Release 05 Scope Reviews
- Install Ramp for Mass Excavation

Upcoming Milestone/Major Dates

- Mass Excavation
- Deep Foundations

EarthCam photo - Court East Demolition

Earth Retention Piles

Earth Retention Piles East of San Camillo

Pile Installation Equipment

February 10 - February 15, 2020

Gilbane Building Company

Feb 03 - Feb 08, 2020

St. Camillus Health Systems Inc.

Phase II Independent Living Tower
Wauwatosa, WI

Current Week Activities

- Start Final Demo / Decoupling of Court East
- Michels Pile Driving Mobilization (Equipment / Tooling)
- NW Lot Site Utilities - North & South Sanitary Main Install
- Court West - South Side - BHM Hole Stabilization
- ERS Bench Cut
- Clear / Grub 103rd St. - Prep for Berm Install
- Site Access Road Construction

Upcoming Week

- Finish Court East Demolition
- Start ERS Pile Install & Lagging
- ERS Bench Cut
- Court West Soil Backfill - Weather Dependent
- Finish Sanitary Main - NW Site - North Main
- Start Berm Placement - 103rd St.
- Continue Rough / Framing / Grading NW Parking Lot
- Start Storm Tie In by Kathy's House

Upcoming Milestone/Major Dates:

- Court East Demo
- Mass Excavation

Gilbane
